

# PROJECT OVERVIEW

MON 05/01/15 WED 04/07/18

% COMPLETE

47%


## MILESTONES DUE

Milestones that are coming soon.

Name	Finish
Launch of Information Clearing House Facility	Mon 03/10/16

## % COMPLETE

Status for all top-level tasks. To see the status for subtasks, click on the chart and update the outline level in the Field List.

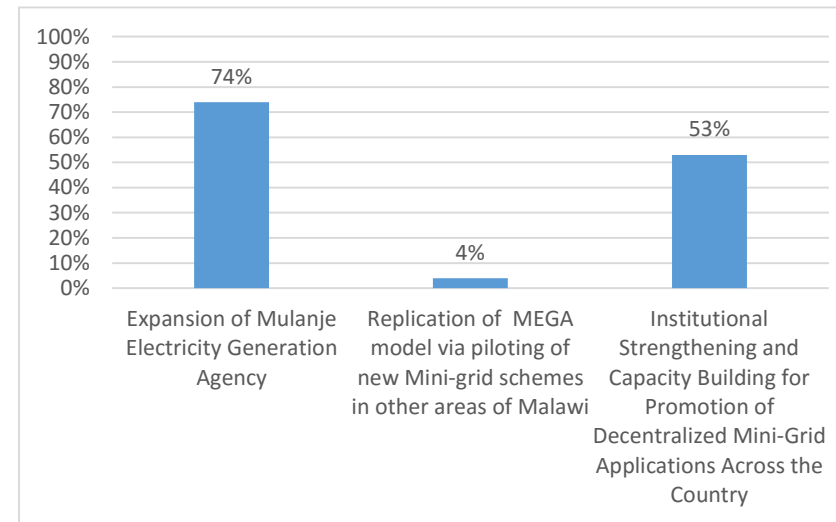

## LATE TASKS

Tasks that are past due.

Name	Start	Finish	Duration	% Complete	Resource Names
Installation of Mini Grid Transmission and Distribution Network	Mon 08/08/16	Fri 27/10/17	16 mons	80%	MEGA
Household Connections	Mon 05/01/15	Fri 15/06/18	45 mons	53%	MEGA
Orientation of Awardees	Mon 26/09/16	Fri 07/10/16	2 wks	20%	PM
Detailed Feasibility Studies and Business Plan Development	Mon 10/10/16	Fri 02/12/16	2 mons	40%	BOO 1
Mini Grid Power Generation, Transmission and Distribution System Designs	Mon 10/10/16	Fri 30/12/16	3 mons	40%	BOO 1
Conduct an Environmental and Social Impact Assessment (ESIA)	Mon 05/12/16	Fri 27/01/17	2 mons	20%	BOO 1
Application for	Mon	Fri 16/06/17	6	0%	BOO 1

Application for Generation and Distribution Licence	Mon 02/01/17	Fri 16/06/17	6 mons	0%	BOO 1
Procure goods and services for the installation of Mini Grid Power Generation, Transmission and Distribution System	Mon 02/01/17	Fri 01/12/17	12 mons	0%	UNDP Proc
Detailed Feasibility Studies and Business Plan Development	Mon 10/10/16	Fri 02/12/16	2 mons	0%	BOO 2
Mini Grid Power Generation, Transmission and Distribution System Designs	Mon 10/10/16	Fri 30/12/16	3 mons	0%	BOO 2
Conduct an Environmental and Social Impact Assessment (ESIA)	Mon 05/12/16	Fri 27/01/17	2 mons	0%	BOO 2
Application for Generation and Distribution Licence	Mon 02/01/17	Fri 16/06/17	6 mons	0%	BOO 2
Procure goods and services for the installation of Mini Grid Power Generation, Transmission and Distribution System	Mon 02/01/17	Fri 01/12/17	12 mons	0%	UNDP Proc
Provide financial support to 1st mini-grid operator to develop & implement EMPs, training staff and communities on O&M, develop and implement innovative payment system and provide information on case study and tool kit	Mon 26/09/16	Fri 29/06/18	23 mons	0%	PM
Provide financial support to 2nd mini-grid operator to develop & implement EMPs,	Mon 26/09/16	Fri 29/06/18	23 mons	0%	PM

training staff and communities on O&M, develop and implement innovative payment system and provide information on case study and tool kit						
Development of compendium of potential district Mini grid trading centres/communities	Mon 07/03/16	Fri 22/06/18	30 mons	10%	DEA	
International Learning Visits to countries in different regional blocks learning on decentralised mini grids experiences, policy and regulations	Mon 17/10/16	Fri 28/10/16	2 wks	0%	PM	
Operationalise Renewable Energy Website and enable linkages to stakeholders	Fri 01/04/16	Thu 15/09/16	6 mons	90%	UNV COMMs	
Update of potential Mini Grid sites	Mon 02/01/17	Fri 18/05/18	18 mons	40%	REIAMA,DEA	
Support to stakeholders in maintaining/Updating RE websites on Mini Grid developments	Mon 02/01/17	Fri 18/05/18	18 mons	20%	PM	
Launch of Information Clearing House Facility	Mon 03/10/16	Mon 03/10/16	0 days	0%	PM,UNV COMMs	
Engage local consultant to develop case studies and tool kit on mini-grids	Fri 01/07/16	Thu 15/12/16	6 mons	40%	PM	
Monitoring of progress on Mini-Grids under development	Thu 01/10/15	Wed 04/07/18	36 mons	50%	DEA	
Dissemination of	Mon	Fri 16/12/16	1 wk	0%	PM	

Dissemination of Mini-Grids Case studies through National Workshop	Mon 12/12/16	Fri 16/12/16	1 wk	0%	PM
Support finalisation of Revision of Energy Policy in include RE Mini Grids development including validation workshop	Fri 01/01/16	Thu 08/09/16	9 mons	90%	DEA
Develop policy and regulatory changes to existing rural electrification policies & regulations	Fri 01/07/16	Thu 01/06/17	12 mons	70%	MERA
