

Annual Progress Report

2007



Development by the people



AREA DEVELOPMENT PROGRAMME BALOCHISTAN

Contents

Executive Summary

1. Project Issues	1
2. Project Performance	2
Output 1 Community Development.....	2
Output 2 Agriculture Development.....	5
2.1 Crop Productivity & Rangeland Management	5
2.2 Livestock	7
Output 3 Water Conservation & Management.....	10
Output 4 Monitoring, Media & Publication	14
4.1 Monitoring & Evaluation	14
4.2 Media & Publication	14
3. Summary of Achievements 2007.....	15
4. Annual Work Plan 2007.....	17
5. Annual Work Plan 2008.....	21

Annexes

1. List of community organizations.....	23
2. Status of water harvesting structures.....	27
3a . Profile of breeding bulls.....	28
3b. Profile of breeding rams.....	29
3c. List of Goat Distribution.....	31
3d. List of chicks birds distribution.....	33
4. List of PSI Schemes.....	37
5. List of Sewing Machines distribution.....	38

List of Tables

Community Development

1. CO Formation	2
2. Trainings	2
3. Skill Development Training	3
4. Status of CO Formation and Membership	3
5. An overview of Quality Criteria of Social Mobilization	4
6. Financial Status Community Mobilization	4

Agriculture Development (Crop Production & Rangeland Management)

7. Training	5
8. Distribution & Demonstration	5
9. District-wise Break-up of Water Harvesting Structures	5
10. An overview of Quality Criteria of NRM Activities	6
11. Financial Status NRM	6

Agriculture Development (Livestock)

12. Training	7
13. Distribution & Demonstration	8
14. Expected outcome of major interventions	8
15. An overview of Quality Criteria of Livestock Activities	9
16. Financial Status Livestock	9

Water Conservation & Management

17. Physical Infrastructure	10
18. Training	10
19. Status of PSI Schemes	11
20. Expected outcome of major interventions	11
21. An overview of Quality Criteria of Irrigation & Water Resources	13
22. Financial Status Water Conservation & Management	13

Monitoring, Media & Publication

23. Media/Publication Activities	14
--	----

List of Figures

Community Development

1.1 Community Development Trainings	3
1.2 CO Savings District-wise	3

Agriculture Development

2.1 NRM Targets/Achievements	6
2.2 Livestock Training (Targets/Achievements)	8

Water Conservation & Management

3.1 Increase in water discharge through Karez Rehabilitation	12
3.2 Water Conservation through Water Storage Reservoir/Channel Lining	12
3.3 Water Conservation (Commulative).....	12

List of Acronyms & Abbreviations

ADPB	Area Development Programme Balochistan
CDO	Community Development Officer
Cft.	Cubic Feet
CMST	Community Management Skills Training
CO	Community Organizations
GoB	Government of Balochistan
M&E	Monitoring & Evaluation
MIS	Management Information System
NRM	Natural Resources Management
SM	Social Mobilization
TBA	Traditional Birth Attendants
UMB	Urea Molasses Blocks
UNDP	United Nations Development Programme
UPVC	Un-plasticized poly vinyl chloride
WFP	World Food Programme of the United Nations
WHS	Water Harvesting Structures

Executive Summary

This is the first annual report of the Area Development Programme Balochistan (ADPB) since inception of its second phase in July 2006. The Phase-II of the programme is spread over four years, ending in June 2010. The period from 1st July to 31 December 2006 was utilized for formally closing Phase-I of the programme and completing institutional arrangement for Phase-II, such as preparation and processing of Project Document and PC-I of the programme, signing of cost-sharing agreement for phase-II between Government of Balochistan (GoB) and United Nations Development Programme (UNDP) for second phase of ADPB and another agreement between ADPB and World Food Programme (WFP) and hiring programme staff. ADPB is a multi-donor programme, funded by the GoB, UNDP, WFP and the beneficiary communities.

The ADPB is community based area development programme, which has two major objectives: a) to reduce poverty in the target areas through livelihoods improvement and, b) to develop sustainable development models for replication. Since livelihoods in the rural areas of Balochistan are mainly dependent upon Livestock, subsistence agriculture and water and irrigation, hence major development interventions of ADPB for livelihoods improvement are also in these sectors. As the programme follows participatory development methodology, therefore launch of all interventions are preceded by community mobilization through formation of Community Organizations (COs), both for male and female beneficiaries. The programme operations are being implemented in pre-selected Union Councils in nine districts of the province, for details see overleaf map.

The programme interventions were formally launched in May 2006, after a delay of five months due to certain procedural hiccups. The total outlay, including development and support expenditure, planned for 2007 was US \$ 1.085 million. By the end of the year, at 85.18 percent utilization, total expenditure stood at US \$ 923,862, out of which about 68 percent went for development expenditure and the remaining was spent on support expenditure. And by that corollary, we were able to implement almost all of our major development interventions.

Community Development was the pioneering intervention and as per our annual work plan we raised 320 male and female community organizations for mobilizing about 3640 households, with a population of over 25,480 people. Since active participation in development involve actual initiation of activities by the people, hence right after the formation of COs, the office bearers and other members were trained on objectives and rationale of organizing themselves, techniques of participatory development, need identification and prioritization, and ADPB's developmental interventions and their implementation methodologies. By the end of the year we trained over 2000 community activists. Besides laying sub-structure for implementation of other programme

interventions, the Community Development Sector also arranged training of 205 women on traditional birth attending services and another 140 women on cutting and sewing skills.

As mentioned above, the main thrust of the programme interventions is focused on improving productivity of the existing agriculture and livestock sectors in the project valleys and to scale-up their base, two activities crucial to improve livelihoods in the rural areas. To this end development interventions in three inter-related sectors of livestock, water and irrigation and natural resource management were undertaken with active participation of the beneficiary communities. All major interventions were undertaken with the communities on cost-sharing basis, ranging from 10 to 30 percent of the cost of interventions. In total the communities contributed Rs 5.00 million towards the development interventions.

In livestock sector, interventions were focused on treatment/vaccination of farm animals, distribution of improved variety poultry birds and dairy goats among poor rural women, breed improvement, capacity building and strengthening and improving livestock extension services in the project areas. By the end of the year we vaccinated over 104,209 farm animals, distributed 2640 poultry birds and 75 dairy goats among 295 poor rural women, distributed 46 improved varieties of animals among herders for breed improvement and trained 1375 people on livestock management. An amount of US \$ 113,548.52 was allocated for livestock sector, of which US \$ 91,010 was expended at 76.06 utilization rate. Details of sectoral interventions and achievement may be seen in the report.

Major interventions implemented under the water and irrigation sector included rehabilitation of karaizes & springs, construction of lines water reservoirs and channel, clean drinking water supply schemes and introduction of high efficiency irrigation system. In total implementation of 49 schemes undertaken at a cost of US \$ 271,185 out of which communities contributed US\$ 72,859 at 30 percent cost-sharing basis. As result of interventions, water availability was increased from 75,044 cft to 105,925 cft, with this increase an additional 400 acres of land is estimated to be brought under the plough.

Under the natural resource management sector this year were constructions of water harvesting structures (also called *khuskaba bandat*) to avail flood/rain water for agriculture/cropping and installation of green houses for establishing nurseries for introduction of improved varieties of fruit trees. Against an annual target of 300 acres, we constructed water harvesting structures over 437 acres, while five modern green houses were installed in Loralai, Muslim Bagh and Kalat.

Timely availability of data and its systematic analysis is indispensable for effective monitoring of programme interventions and to ensure achievement of qualitative and quantitative targets of the programme. To this end comprehensive baseline survey of project areas and a web-based management information system were planned in the annual work plan of 2007. The contract for developing MIS has been awarded to the successful bidder, while process for award of contract for baseline survey is underway and shall be concluded soon.

The total cost of annual work plan for 2008 is US\$ **1,504,746, almost 40 percent over by annual work plan of 2007, with corresponding increase in all major interventions.**

Experiential learning and community perspective remained guiding principles with ADPB management both in the implementation of interventions and designing of the new ones. We have not only been involved in implementing development interventions but also engaged with our partner communities in creating new knowledge to improve those practices and make them best suited to their contexts. Communities are more than willing to participate in the development interventions and contribute in kind and cash towards those efforts provided they are let to set the priorities and lead processes for implementation of those interventions. In 2007 our partner communities contributed Rs 5.00 million for development initiatives, which testifies to the inclusivity of ADPB's development approach and activism of the communities in the process and ownership of the interventions.

1. Project Issues

Status of project risks

1. Operational:

Process Efficiency: The project faced certain procedural/administrative hiccups, especially related to the recruitment of staff, approval of work plan and release of funds to the project by co-donors. These hold-ups did take toll on achieving annual targets and fund utilization.

Project Design: Uncertainties/difficulties were also not properly appreciated, while project outputs were being designed. Project feel that there is a need to reconsider overall project outputs in the light of past one years experience.

Security issues: The uncertain security environment in the province during the past year reduced staff mobility & accessibility almost in all districts, which also affected our performance.

Logistics: Due to scattered patterns of population settlements, field works involve traveling long distances on hilly/dirt tracks. The project vehicles are quite old and their fuel consumption is on the higher side. In addition, these old vehicles require frequent repair and maintenance. With the recent increase in the fuel prices, it seems that the share of support cost in overall project expenditure will also increase in the coming years.

2. Financial:

Inflation: The cost of construction material including cement, steel, bricks and PVC pipes and fittings and their transportation cost has increased which will also reflect on the cost of project activities especially that of productive and social infrastructure (PSIs) schemes.

External: More than half of annual funding is to be contributed by the Government of Balochistan, being the major cost sharing donor to programme. However so far the governments track record is not much encouraging. In 2007 it contribution was less than 50 percent of the committed funding, in 2008 it may be even less. Secondly, beneficiary communities are co-financing in assets and infrastructure building activities and contributed PKR 0.5 million towards these activities in 2007. However, high energy prices and drought-like situation may affect their income which may in turn constrain their contributions to programme costs.

3. Institutional:

In 2007 the project faced difficulty in hiring skilled staff for the positions of junior engineers, monitoring officers and female social mobilizers. The pool of skilled professionals in the province is quite limited and with increasing demand for such professionals, the project may even face turnover of the existing ones.

4. Political:

After the February general elections in the country, the new government is about to take over power in the province. Although the contractual obligations will be binding and honored too, yet the project may face difficulties in funds flow/ partnership in the transition period or even after if there is switch in governments priorities or it faces a financial crunch.

Open project issues

1. Community share

The project faced difficulty in mobilizing Community Organization to contribute their share for development projects (PSI). An analysis of mobilizing strategy revealed that our techniques were theoretical and not properly embedded in the framework of programme interventions and methodology. Once it got reviewed and modified mobilizing strategy, Community Organizations found willing to contribute their share towards developing projects. Total community contribution in 2007 for developmental interventions was Rs 5.00 million.

2. Sectoral training

Some of our trainings were also theoretical in nature. It was observed that skills being imparted were either not or marginally employable in improving livelihoods of the trainees, as they didnt have requisite assets/resources to make use of those skills. As learning now all our trainings are for the optimal utilization of the assets/projects created through our developmental interventions or on the specific demand of the communities

3. Nature of PSI


User perspective has led us to modify Productive Social Infrastructure projects planned for implementation with the COs. The project have had to do away with certain kinds of PSIs, such as construction of stock water ponds, earthen dams, and reduce quantum of others such as increasing allocations for water harvesting structure, construction of lined water storage ponds and channels and rehabilitation of karazes. In a way, now our PSIs are more demand-driven in planning and design than previously.

4. Availability of technical staff

During reporting year the project faced dearth of technical staff particularly junior engineer and female social organizers for remotest districts.

CO Formation

- First contact meeting with Community
- Introduction of the Programme and Process
- Development of Village Profile through social mapping
- Formation of Community Organization,
 - selection of President and Secretary of CO
 - signing of MoU between CO and ADPB
 - oath taking
- Impart Community Management Skills Training (CMST) to the CO members focusing on rationale and benefit of organizing, basic principles of participatory development, need identification and prioritization, ADPB's programme implementation methodology and basic office management and record keeping skills.

**2. Project Performance****Output 1: Community Development**

The community development is a key component of Area Development Program, which plays central role in laying substructure for implementation of all programme interventions. The main objective of this sector is to organize the target population into community organizations, and mobilize them around programme's philosophy through a dialogue process for active participation in developmental interventions. Keeping in view the prevailing cultural and social milieu in the province, separate community organizations for men and women are formed at village level. (Annex 1)

Since active participation by the communities in developmental activities involves steering the entire course of implementing developmental interventions- from need identification through resource mobilization to execution- hence, right after formation of COs, the office bearers and some other members are given capacity building training called Community Management Skills Training. In this training the community members are trained on objective and rationale of organizing themselves, participatory development and mobilizing techniques, need identification and prioritization, ADPB's programme implementation methodology and basic office management and record keeping. The capacity building of COs is further enhanced through series other training events. The COs set their needs and priorities regarding all programme developmental interventions, which are implemented on cost-sharing basis, which are articulated and presented through formal resolutions.

Besides organizing and mobilizing communities for programme's development interventions, this sector also arranges women-specific interventions to improve access to and quality of social services at local levels and create assets for rural women under World Food Programme's contribution. These include imparting trainings to female activist/service providers on health and hygiene and traditional birth attendant services and cutting and sewing skills. 205 women were trained on TBA skills and 140 women trained on cutting and sewing skills. The would-be tailor-women were also given sewing machines with necessary sewing kits, free of cost through WFP assistance (Annex 5).

As per our estimates, a semi-skilled tailor-woman stitches around 8-10 pairs of shalwar kameez per month and charges about Rs 50- 60 per pair. Estimated annual income of single semi-skilled tailor-woman would be over Rs. 600. Similarly in rural areas a TBA practitioner charges around RS 1500 per delivery case and annual estimated income of TBA would be over Rs 15,000.

Targets:**a: CO Formation**

Activity	Target	Achievement	%
CO Formed	320	336	105

b: Trainings

Activity	Total	Achievement	%
CMST	2040	2149	105
Wool Spinning	30	---	-
Cutting & Sewing	195	140	71.8
Training of SM/CDO on community based approaches	40	---	-

c: Skills Development Training

Activity	Target	Achievement	%
TBA	220	205	93.18
Health & Hygiene	790	934	118.2
Embroidery Training	60	60	100

Start & End Date: May December 2007
% Progress: 90%



Figure 1.1 Community Development Trainings

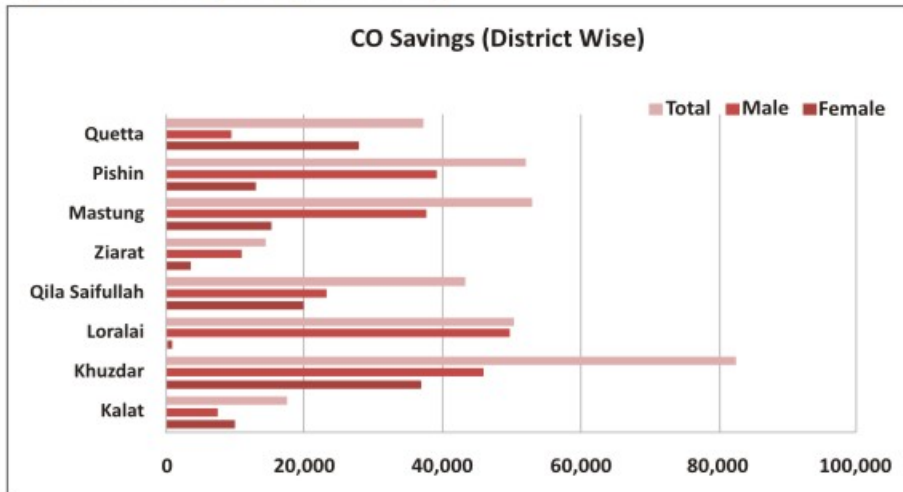


Figure 1.2 CO Savings (District-wise)

Status of CO Formation and Membership


Regions	Districts	CO Formation			Membership			Household
		Female	Male	Total	Female	Male	Total	
Khuzdar	Kalat	23	18	41	406	351	757	351
	Khuzdar	25	24	49	391	376	767	340
	Sub-total	48	42	90	797	727	1,524	691
Loralai	Loralai	16	20	36	243	280	523	300
	Qila Saifullah	17	23	40	259	334	593	403
	Ziarat	17	23	40	258	373	631	372
	Sub-total	50	66	116	760	987	1,747	1,075
Quetta	Mastung	18	26	44	307	475	782	522
	Pishin	15	28	43	172	394	566	432
	Quetta	23	20	43	433	345	778	389
	Sub-total	56	74	130	912	1,214	2,126	1,343
Total		154	182	336	2,469	2,928	5397	3,109



CO Savings

The interactions with communities and periodic calendar meeting with COs have been very engaging. 100% COs raised its saving, the cumulative saving amount is PKR 350,119. Among this Rs. 126,744 have been raised by women COs. All COs have been imparted training on importance of Saving and proper record keeping.

An Overview of Quality Criteria Social Mobilization



Activity	Quality Criteria	Date	Results of Activities		
			User Perspective	Resource Status	Timeliness
CO formation	At least 80% of the households in a village are members of a community organization.	May-December 2007	336 COs were raised in 2007. On average a CO comprises 20-25 households and every HH has a representation in the CO.	All resources including HR were utilized properly	Targets achieved with in given time frame and resources
CMST/LMST	Capacity of CO activists built in community management and participatory development.	May-December 2007	Over 2000 community activists trained on mobilization and participatory development techniques to enable them to take actively participate in development interventions.	Activity completed through an in-house arrangement. Developed Training manual, trained SMs and imparted all trainings through them.	Targets achieved with in given time frame and resources
Skills Development	Impart vocational training to women on traditional birth attending services and cutting and sewing skills as part of income generating activity for rural women.	May – December 2007	206 women trained on TBA skills and 140 women trained on basic sewing and cutting skills. The estimated annual income of a semi-skilled tailor-woman is Rs. 600 while that of a TBA is Rs 15,000.	Master trainers hired from market/Health Department for designing training manual and imparting training to the women. All other requirement met through in-house resource management	Targets achieved with in given time frame and resources

Financial Status Community Development

	Donor	Account	Budget	Expenditure	Balance
COMMUNITY DEVELOPMENT	UNDP	63405	24152	17363.98	6788.02
	GOB		9227	9227	
	WFP		23762.50	21520	2242.50
	Total			57141.5	48110.98

Agriculture Development

Output 2: Agriculture Development

Output 2.1: Crops Productivity & Rangeland management

This sector aims to harness and develop available natural resources for improving livelihoods in the programme districts. Two important developmental interventions undertaken under the NRM this year were construction of Water Harvesting Structures (WHS), also known as *khuskaba bandat* and installation of green houses for establishing nurseries for introduction of improved varieties of fruit trees. Under the first intervention, over 437 acres of water harvesting structures were constructed to avail rain water for agriculture and cropping. (Annex 2)

For introducing improved varieties of fruit trees and assisting in establishing modern commercial fruit nurseries in the project districts, five greenhouses, each having a capacity of 17,000 saplings, were installed in Loralai, Muslim Bagh and Kalat. The greenhouses shall be utilized for Interventions for improving rangeland vegetation cover would increase the livestock carrying capacity and overall ecological support system. These greenhouses shall be used specifically for making available improved varieties of almond, apple and olive sapling for the orchid's growers in the programme districts.

In addition to undertaking above developmental activities, a number of capacity building trainings, focused on improving the skills of rural women, introducing kitchen gardening and nursery raising techniques were also arranged. Details of developmental activities and training events undertaken by the NRM sector during 2007 are given in the tables below.

As per the estimates of the Provincial Agriculture Department, annual average wheat yield of an acre of water harvesting structure is around 600 Kg. At present a Kilo gram of wheat is selling about Rs 20.00. Hence as per our estimation, average annual income of single WHS would be around Rs 12,000.

Targets

a: Training

Activity	Target	Achievement	%
Nursery raising / plantation management techniques	100	100	100
Program/ line department staff on NRM	60	47	78.33
Stone dressing/Pitching and wire weaving techniques	120	100	83.33
Grazing management technique	100	100	100
Kitchen Gardening	100	80	80

Distribution and Demonstration

Activity	Target	Achievement	%
plant production (nursery raising)	0.08 mil. seedling	0.060 mil. Seedling	75
Planting of palatable trees and shrubs on rangeland (Forage Reserves)	180 Acres	10	5.5
Water Harvesting structures	300 Acres	437	146

District-wise break-up of Water Harvesting Structures

District	Acres
Mastung	222
Khuzdar	140
Kalat	20
Quetta	27
Loralai	28
Total	437



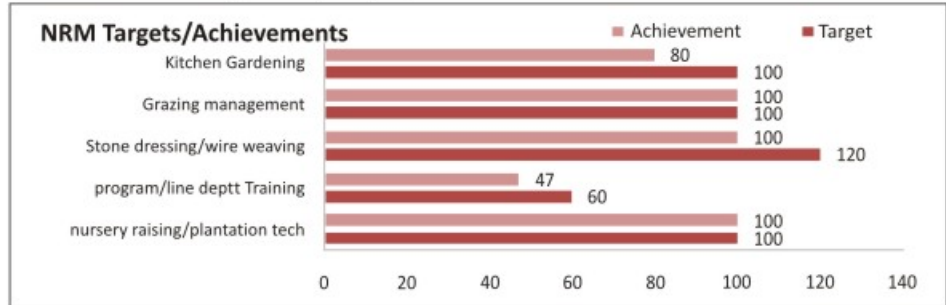


Figure 2.1.1 NRM Targets/Achievements

An Overview of Quality Criteria and Results of NRM Activities

Activity	Quality Criteria	Date	Results of Activities		
			User Perspective	Resource Status	Timeliness
Trainings	Skills imparted for improved livelihoods.	May-December 2007	427 community activists trained on these skills, which are relevant to improving their livelihoods.	Market trainers hired for developing training material and imparting training to community acitivits.	Targets achieved with in given time frame and resources
Demonstration/ Distributions	Improved NRM practices demonstrated and promoted.	Dec'07	5 Green houses were installed in Muslim Bagh, Loralai and Kalat districts. About 17000 saplings per greenhouse will be developed in 2008.	GH were provided by WFP installation supplemented by UNDP/ GOB resources.	do
PSI	Community based rainwater harvesting structures developed and operational.	Dec'07	Water harvesting structures constructed on over 437 acres in Mastung, Khuzdar and kalat districts. On average a single acre of WHS produces 600 kg of wheat at an average annual income of Rs 12,000.	Community contributed 30% share in cash and kind, remaining cost met through UNDP/ GoB resources	do



Financial Status NRM

	Donor	Account	Budget	Expenditure	Balance
NRM	UNDP	63405	36242	34453.75	1788.25
	GOB		4722.55	7422.55	0.00
	WFP		16175	6790	9385
	Total		57139.55	48666.3	11173.25

Livestock

Output 2.2: Livestock

Raising livestock is one of the major activity and source of livelihood of people living in rural areas of the province. Over the years due to socio-ecological changes and long spells of drought, the ranges- which provide 60 to 70% grazing for livestock, particularly for small ruminants- have been depleting resulting in poor feed pool. Feed shortage from overgrazed rangelands, low agriculture produce especially during winter, incidence of epidemic and parasitic diseases, and inappropriate breeding and marketing systems are the serious setbacks towards an efficient animal production in ADPB Programme Districts/Valleys.

In view of prevailing situation the Livestock and Fodder Production Sector interventions focused on vertical as well as horizontal increase in livestock production through breed improvement, reduce livestock morbidity and motility through vaccination and de-worming, strengthen livestock service delivery in the rural areas and by creating livestock assets among the poor rural women through distribution of improved varieties of egg-laying chickens and goats on cost-sharing basis. In our effort to improve breed of existing animals in the project valleys (Annex 3a, 3b), we distributed 46 animals of improved varieties among the local breeders. The biggest demand of the communities on our resources was for vaccinating and de-worming the animals: We vaccinated and de-wormed over 100,000 animals in project valleys. For improving livestock services in the project valleys, we strengthened 11 existing dispensaries by providing necessary equipment and training to staff. We also trained 18 activists from project valleys as community livestock extension worker at the provincial livestock institute.

As part of capacity building exercise, the livestock sector arranged training for 1375 persons (188 Men and 1187 Women) on livestock management and fodder production. Rearing household goats and keeping farm chicken in the rural areas is predominantly women's occupation. Availing this opportunity for increasing income at household levels, the livestock sector distributed 75 high yielding goat (Annex 3c) and 2640 rural poultry birds (in sets of 12 birds) among poorest women on 10% cost-sharing basis. The details of training imparted to community members, animals vaccinated, goats and chicken distribution and other interventions are given in the tables below.

a: Training

Activity	Target	Achievement	%
Livestock management	118	98	83
Improved rural poultry farming	600	585	97.5
Improved dairy farming	240	220	91.6
Sheep and goat raising and reproduction	240	269	112
Straw treatment and storing	30	30	100
Periodic free vaccination	20,000	61753	-
Programme/line deptt. staff in animal reproduction, nutrition, livestock management.	50	53	106
Deworming campaign against contagious/infectious diseases and external & internal parasites	20,000	42,456	212
Awareness on animal health and hygiene	60	60	100
Awareness on nutrition and feeding practices	100	60	60





Figure 2.2.1 Livestock Training (Targets/Achievement)

b: Distribution & Demonstration

Activities	Target	Achievements	%
High yielding Goat plus provision for vaccination, feed, quarantine.	75 Goat	75	100
Distribution of Chickens of Fayoumi, Red Rhode/golden type among women for establishing backyard poultry farms.	2640 Birds	2640	100
Breed Improvement through artificial insemination & natural mating (6 Bulls & 18 Rams)	24	46	191
Demonstration, fattening			
a. Lamb kids	600	600	100
b. Calves	30	30	100
c. Ewe flushing	2000	2000	100
Veterinary Kits to trained farmers/community workers	9 Kits	18	200
Demonstration Plots for introduction of Alfa-Alfa/Napier/elephant grass, hybrid sorghum, mot grass; cost of seed, fertilizer irrigator – 37 units in 37 Cos.			
Urea Molasses	2000 UMB	4285	214
Strengthen delivery of existing Livestock Dispensaries	11 Dispensaries	11	100

Expected Outcomes of Major Interventions

S. No	Activities	Total	Monitory benefits US\$	
1	Vaccination and deworming	104191 animals	5% decrease in mortality: 5210 animals @ 5000/animal=26050000/-	434166
2	Poultry distribution	2640 birds	1540 eggs daily x 275 days @ Rs.5= 7700 x 275 days: 2117500/-	35292
3	Goat distribution	75 goats	Daily 2.5 liter milk x 75 x 305 days: 188 liter @ Rs.30= 5640 x 305= 1720200/- Annually 75 kids @ 3000=2250000/-	32420
4	Breed improvement	46 animals	One breeding animal cover 50 animals: 46x50=2300 animals @ Rs. 50 fee/animal=1150000/-	1917
5	Fattening	630 animals	Daily weight gain of 250 gram x 60 days=15 kg @ Rs. 220/kg=2079000/-	34650
6	Ewe flushing	2000 animals	10% increase in lambing: 200 animal @ Rs. 3000=600000/-	10000
7	Veterinary kits	18 kits	Income generation of the CLEWS: Rs. 1000/month x 18x12=216000/-	3600
8	Fodder production	30 acres	10% production increase @ 500/acre=Rs. 150000/-	250
9	Urea Molasses Blocks	4285 UMB	1 animal need 6 UMB for 60 days with an increase of body weight @ 100 gram daily=6 kg x 714 x Rs. 220= 942480/-	15708
G. Total			568003	

Start & End Date: June December 2007

% Progress: 95 %

Overview of Quality Criteria and Results of Livestock Activities

Activity	Quality Criteria	Date	Results of Activities		
			User Perspective	Resource Status	Timeliness
Trainings	a) Rural poultry and dairy farming management, raising and reproduction techniques improved; b) A cadre of community livestock extension workers developed to improve livestock delivery services in project areas.	June to December 2007	a. 1375 community activist trained in different trades. b. 18 community activists trained as community livestock extension workers for improving livestock delivery services in project areas.	Qualified master trainers hired for imparting trainings to community activists. Community livestock extension workers training arranged at Animal Sciences Institute Quetta.	Targets achieved within given timeline
Demonstration/ Distributions	Backyard poultry farming promoted as an income generating activity.	May-December 2007	2640 poultry birds and 75 dairy goats distributed among 220 and 75 poor rural women respectively. 295 HH benefited from the activity.	10% of cost contributed by the beneficiary while remaining cost met from UNDP and GoB resources.	...do...
Animal Vaccination and deworming campaign	Timely provision of services for reducing animals morbidity and mortality.	June-December 2007	Over 100,000 farm animals vaccinated and de-wormed. 5% estimated reduction in mortality.	Vaccines funded through ADPB resources. Technical services of line department and Community livestock extension workers utilized.	...do...
PSI	Capacity built of line departments in enhanced service provision.	May-December 2007	11 existing dispensaries strengthened by providing necessary equipment and training to staff.	Equipment provided through ADPB funds and master trainer hired for training staff.	...do...




Financial Status Livestock

	Donor	Account	Budget	Expenditure	Balance
Livestock	UNDP	63405	89057	62162.29	26894.71
	GOB		16191.52	14944.46	1247.06
	WFP		8300	4005	4295
	Total		113548.52	81111.75	32436.77



Water Conservation & Management

Output 3: Water Conservation & Management



Majority of the people in rural areas of the province are associated with agriculture for earning their livelihoods. The quality and quantity of agriculture produce depend on the availability of water, which is invariably scarce in the province. Therefore, interventions aimed at developing irrigation water resources for increasing and conserving water, are central to any programme for improving livelihoods in the rural areas.

Four kinds of interventions were undertaken under the Water and Irrigation sector for developing water resources in the project areas for improving and conserving available water. These were: a) Development and rehabilitation of karez and springs; b) Construction of lined water storage reservoirs and channels; c) Introduction of high efficiency irrigation systems such as bubblers and trickle irrigation systems, and; d) Clean drinking water supply schemes (Annex 4). In 2007 a total of 50 schemes, under the above interventions, were undertaken in the project district at a cost of Rs. 16.38 million, out of which Rs 4.4 million were contributed by the beneficiary communities.

As regards impact of interventions, under karez rehabilitation in six schemes water availability increased from 8200 cft to 16800 cft, which is an increase of 104%. 22 schemes of constructing lined water storage reservoirs and channels were undertaken, which resulted in increasing volume of available water from 66844 cft to 89,125 cft (cumulative increase from 75044 to 105,925 cft.) hence we were able to conserve about 41% of available water, as a result over 400 acres of new lands will be brought under cultivation. We also constructed 15 water supply schemes through which clean drinking water shall be available to over 2000 people. District-wise details of schemes, their costs and estimated benefits are given in the tables below.

Targets: Physical Infrastructure

Activities	Target	Achievements	%
Livestock Water Ponds	1 Pond	1	100
Irrigation Water Courses	34 Schemes	43	126
Solar & wind based irrigation system and solar lanterns	1 Schemes	1	100

b: Training

Activities	Target	Achievements	%
Jr. Engineers , Lin Deptt. Staff on designing/implementation of infrastructure schemes.	10 Persons	2	20
Efficient use of water for irrigation	30 Persons	24	80

Start & End Date: May December 2007

% Progress: 100%

Status of PSI Schemes

Activity	Schemes	Cost			Beneficiaries
		Community	ADPB	Total	
Lined Water Storage Reservoir, Channel & UPVC Pipe for Agriculture Purpose	22	2,936,414	6,850,937	9,787,351	2415
Water Supply Schemes	15	965,545	2,252,946	3,218,491	1792
Karez Rehab.	4	314,212	733,163	1,047,375	448
Spring Rehab.	2	55,114	128,598	183,712	189
High Efficiency Irr. System	5	130,860	913,168	1,044,028	35
Solar & Wind Based Energy System	1	-	1,104,000	1,104,000	840
Total		4,402,145	11,982,812	16,384,957	5719

Expected Outcomes of Major Intervention

Districts	Total Irrigated Area Before Intervention (Acre)	New Irrigated area increase after intervention (Acre)	Total Irrigated area after intervention (Acre)
A. Lined Water Storage Reservoir, Channel & UPVC Pipe for Agriculture Purpose			
Pishin	215	90	305
Quetta	50	15	65
Qila Saifullah	114	98	212
Loralai	63	20	83
Ziarat	105	35	140
Sub-total (A)	547	258	805
B. Karez Rehab			
Qila Saifullah	33	60	93
Khuzdar	40	15	55
Sub-total (B)	73	75	148
C. Spring Rehab			
Loralai	63	30	93
Khuzdar	60	40	100
Sub-total (C)	123	70	193
Grand Total (A+b+C)	743	403	1146



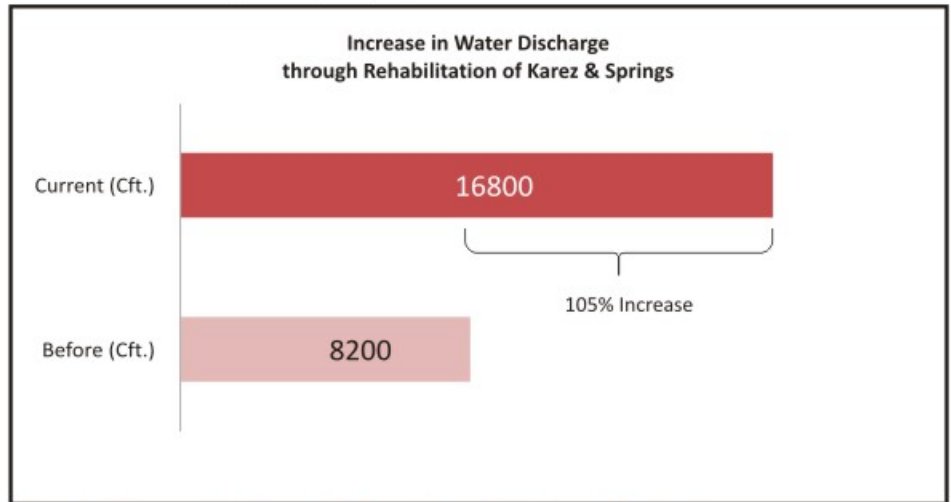


Figure 3.1 Increase in Water Discharge Through Karez Rehabilitation

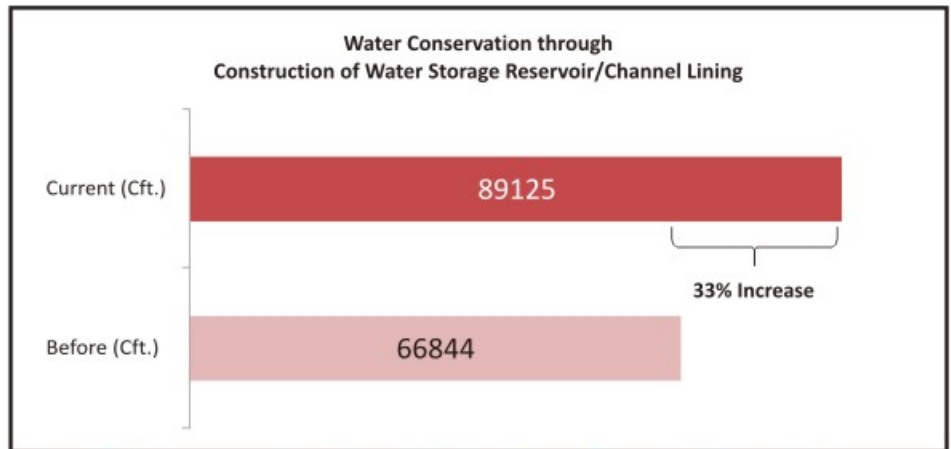


Figure 3.2 Water conservation through Water Storage Reservoir/Channel Lining

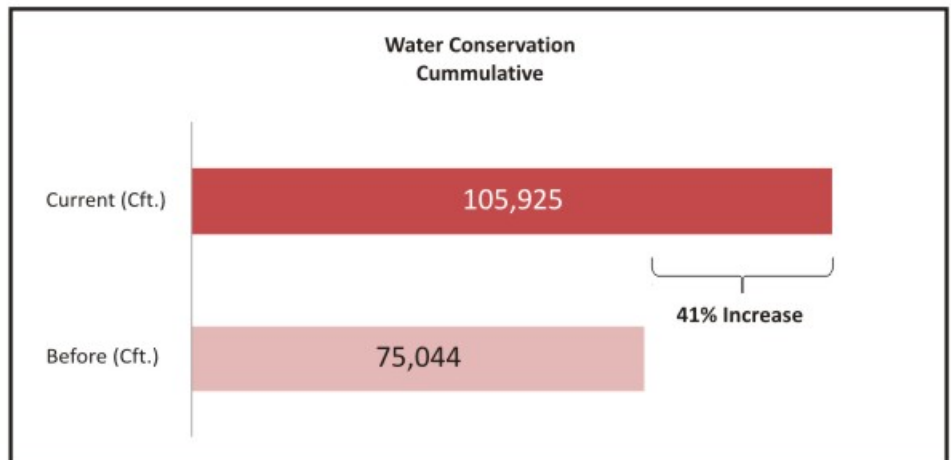


Figure 3.3 Water conservation

An Overview of Quality Criteria Irrigation & Water Resources

Activity	Quality Criteria	Date	Results of Activities		
			User Perspective	Resource Status	Timeliness
Trainings	Farmers trained on efficient use of water for irrigation	May-December 2007	24 farmers trained	In-house arrangement and organization resources used for this activity.	Targets achieved within given time frame and resources
Demonstration/ Distributions	High efficiency irrigation system introduced for technology diffusion in project areas.	May-December 2007	5 schemes of HEIS installed in project areas for technology diffusion and skill transfers.	Technical services for hired from market. 15% cost contributed by beneficiaries while remaining cost met from UNDP and GoB resources.	...do...
PSI	Water availability for agriculture increased through development of water resources and conservation.	May-December 2007	49 schemes of lined water storage reservoirs and channels, water supply schemes, and Karaiz and springs development and rehabilitation undertaken.	Beneficiary communities contributed Rs 4.4 million at cost-sharing of 30 % of schemes; the remaining cost was met from ADPB resources.	...do...




Financial Status Water Conservation & Management

	Donor	Account	Budget	Expenditure	Balance
WIS	UNDP	63405	23654	22436	1218
	GOB		206563.88	184374.46	22189.86
	WFP		27550	13830	13720
	Total		257767.88	220640.46	37127.86

Monitoring, Media & Publication

Output 4: Monitoring, Media & Publication

Output 4.1: Monitoring & Evaluation



The main responsibility of the Monitoring and valuation (M&E) sector is to oversee that quantitative and qualitative targets of the annual work plan are efficiently and effectively achieved. To this end, the M&E sector closely followed the pace of implementation of all programmer interventions and regularly informed the Sector Specialists of users' perspective on various programme activities for improvement and course correction. In addition to the mandated functions, the M&E sector also managed and supervised data collection of all programme interventions and beneficiary record. The M&E sector is headed by a Sector Specialist, who is assisted by three Monitoring Officers, on each for the three regions.

Timely availability of data and its systematic analysis is indispensable for effective monitoring of programme activities and ensuring to achieve quantitative and qualitative targets of programme. To this end, development of a comprehensive baseline survey of the programme valleys and a geographic based management information system were proposed in the annual work plan of 2007. The M&E sector drafted the terms of reference for both assignments and called expression of interest from the prospective firms. The contract for developing MIS has been signed with M/S Aman Associates, while process for awarding contract for conducting baseline survey is underway and contract shall soon be awarded to the competent bidder.

Output 4.2: Media & Publication

Media and Publication is a support sector with a mandate to arrange publication of programme introductory pamphlets and brochures for information of the beneficiary communities, disseminate programme mandate and achievement to the media, general public, donor agencies, civil society organizations and respective government departments through posters and booklets. In addition the sector was also responsible for compiling quarterly progress reports and maintaining coordination among all sectors at the head office level. The detail of various promotional material published by the sector is given in the table below.

Material	Sector	Quantity
Promotional Material		
PSI Sign Boards	Water Sector	41
Posters (300 each sector)	Water, Livestock & Social Services	1800
Introductory Material		
Introductory Brochure in Urdu	All Sectors	3000
Shoulder Carrying bags for Field staff	All Sectors	55
	All Sectors	1000
Training Completion Certificates for CO members	All Sectors	3000
COs records keeping Material		
Bachat Bachat/Saving Crds	Social Sector	9200
Bachat Saving Registers	Social Sector	1000
Karwai registers	As above	1200

3. Dsistrict wise Summary of Achievements 2007

S. No.	Activities	Units	Breakup of Achievements										G-Total	
			Loralai	Qilla Saifullah	Ziarat	S.Total	Quetta	Pashin	Mastung	S.Total	Kalat	Khuzdar		S.Total
1) Community Development Services														
1.1	Formed Community Organizations	CO	36	40	40	116	43	43	44	130	41	49	90	336
1.2	persons trained in CMST	persons	334	333	190	857	227	251	169	647	377	268	645	2,149
1.3	persons trained in embroidery	persons	-	-	-	-	60	-	-	60	-	-	-	60
1.4	persons trained in H&H	persons	101	238	30	369	76	58	20	154	176	235	411	934
1.8	Cutting & Sewing training		50			50					35	55	90	140
1.9	TBA Training		18	45	22	85	15	15	15	30	40	50	90	205
2) Natural Resource Management(NRM)														
2.1	Person trained in Stone dressing & Wire weaving techniques.	persons	40	-	-	40	40	-	20	60	-	-	-	100
2.2	persons / programme line department staff trained in NRM	persons	32	15	-	47	-	-	-	-	-	-	-	47
2.3	plant production/nursery raising	plants seedling in million	0	0	-	0	-	-	-	-	0	0	0	0
2.4	Installation of Greenhouses	Numbers	2	1	-	3	-	-	-	-	1	1	2	5
2.5	Planting of platable trees and shrub	Acre	-	-	-	-	-	-	-	-	-	10	10	10
2.6	Water harvesting and spreading	Acre	28	-	-	28	27	-	222	249	20	140	160	437
2.7	grazing management technique	persons	20	20	-	40	20	-	40	60	-	-	-	100
2.8	nursery raising and its management	persons	40	20	-	60	-	-	-	-	20	20	40	100
2.9	Persons trained in Kitchen gardening.	Persons	-	-	-	-	-	-	-	-	40	40	80	80
3) Livestock (LS)														
1 Trainings														
1.1	Livestock management	98 persons	2	42	3	47	2	2	2	6	22	23	45	98
1.2	Improved rural poultry farming	585 persons	100	140	40	280	80	40	40	160	60	85	145	585
1.3	Improved dairy farming	220 persons	60	60	20	140	20	-	-	20	20	40	60	220
1.4	Sheep & goat raising and reproduction	269 persons	80	60	-	140	20	-	27	47	40	42	82	269
1.5	Straw treatment and storing	30 persons	-	-	-	-	-	20	10	30	-	-	-	30
1.6	Awareness on animal health and hygiene	60 persons	20	20	-	40	-	-	-	-	20	-	20	60
1.7	Awareness on nutrition and feeding practices	60 persons	-	-	-	-	-	-	-	-	40	20	60	60
1.8	Programme/Line deptt. staff in animal reproduction, nutrition, livestock management	53 persons	8	3	-	11	13	6	7	26	5	11	16	53
1.9	Periodic free vaccination	61735 animals	4,948	15,926	4,765	25,639	5,682	7,046	2,314	15,042	9,928	11,126	21,054	61,735

3. Dsistrict wise Summary of Achievements 2007

S. No	Activities	Units	Breakup of Achievements											G-Total
			Loralai	Qilla Saifullah	Ziarat	S.Total	Quetta	Pashin	Mastung	S.Total	Kalat	Khuzdar	S.Total	
1.1	Deworming campaigns against contagious/infectious diseases & external and internal parasites	42456 animals	4,848	11,086	4,465	20,399	2,741	5,748	1,057	9,546	7,198	5,313	12,511	42,456
2	Distribution and demonstration:													
2.1	High yielding goats plus provision for vaccination, feed, quarantine	75 goats	10	9	9	28	9	9	9	27	10	10	20	75
2.2	Chickens of Fayoumi, Red Rhode/Golden Type among women for establishing backyard poultry farms	220 sets	27	28	28	83	28	27	27	82	27	28	55	220
2.3	Breed improvement through artificial insemination and natural mating	46 animals	6	6	6	18	6	5	6	17	6	5	11	46
2.4	Demonstration, fattening:													
	a) Lamb kids	600 animals	75	75	75	225	75	75	75	225	75	75	150	600
	b) Calves	30 animals	7	-	-	7	-	7	-	7	8	8	16	30
	c) Ewe flushing	2000 animals	250	250	250	750	250	250	250	750	250	250	500	2,000
2.5	Veterinary kits to trained farmers/community workers	18 kits	2	2	3	7	2	2	2	6	2	3	5	18
2.6	Demonstration plots for introduction of Alfa alfa/Napier/ Elephant grass, hybrid sorghum, Mot grass; Cost of seed, fertilizer, irrigator -37 units in 37 COs	30 acres	3	3	2	8	5	5	5	15	3	4	7	30
2.7	Urea Molasses Blocks (UMB)	4285 UMB	535	535	535	1,605	535	535	535	1,605	535	535	1,070	4,280
2.8	Strengthen delivery of existing livestock dispensaries	11 dispensaries	2	1	1	4	2	2	1	5	1	1	2	11
2.9	Livestock water pond	1 dispensary	1	-	-	1	-	-	-	-	-	-	-	1
4)	Water & Irrigation (WIS)													
4.1	Introduction of approved high efficiency irrigation system	Acres	2	1	1	3	-	-	-	-	2	-	2	5
4.3	Irrigation water courses	ponds	1	6	4	11	1	10	-	11	-	-	-	22
4.4	Distribution of solar lanterns.	Lanterns												120
4.5	Water supply schemes	schemes	1	2	3	3	2	3	5	5	3	4	7	15
4.6	Rehabilitation of Karezes/Springs	schemes	1	3	4	4	-	-	-	-	2	2	2	6
4.7	Jr. Engineers , lin Deptt. Staff on designing/implementation of infrastructure schemes.	Persons	-	-	-	-	-	10	-	10	-	-	-	10
4.7	Efficient use of water for irrigation	Persons	-	-	-	-	-	24	-	24	-	-	-	24

4. ANNUAL WORK PLAN 2007 (UNDP-GOB), Revised.

Key Activities	Target	Responsible Party	Budget Line	Estimated Cost (US\$)	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter		
					Jan.	Feb.	Mar.	Apr.	May	Jun.	Jul.	Aug.	Sep.	Oct.	Nov.	Dec.
1 Community Development.																
a CO Formation:	320						100					120				100
Community Development Supervisors services		SSS		43,825												
Social Mobilizers services		SSS		136,183												
Social Sector and Gender Specialist services		SSS		14,405												
Duty Travel		SSS		7,833												
b Training:																
CO office holders in CMST.	1080 Person	SSS		14,746			100	250	100	100	100	100	150	150	130	
Baseline Survey	1	M&E		4,567			1									
Management Information System	1	M&E		4,566			1									
SM / CDS on community based approaches	40 Persons	SSS		3,500			40									
Sub - Total Community Development				229,625												
2 Natural Resource Management:																
2.1 Crops Productivity and Rangeland Management:																
a Training:																
Nursery raising/ plantation management techniques	100 persons	NRM		933			33					33				34
Programme/ Line department staff in Natural Resource Management	60 persons	NRM		950							40					20
b Distribution and Demonstration:																
Plant Production (nursery raising)	0.08 million seeding	NRM		15,725										0.04	0.04	
Planting of platable trees and shrubs on rangelands (forage reserves).	180 acres	NRM		7,482										90		90
Introduction of High Efficiency Irrigation Systems	5 plots	WIS		15,875								1	1	2	1	
NRM Specialist services				10,129												
National Consultant				0												
Sub - Total Crops Productivity and Rangeland Management				51,093												
2.2 Livestock:																
a Training and campaigns:																
Livestock management.	18 persons	LSS		6,336								6				6
Improved rural poultry farming	200 persons	LSS		6,800			50	50				50				50
Improved dairy farming	40 persons	LSS		2,000			10	10				10				10
Sheep & goat raising and reproduction.	40 persons	LSS		2,000			10	10				10				10
Straw treatment and storing.	30 persons	LSS		1,500								10	10			10
Grazing management techniques	100 persons	NRM		933				25	25					25		25
Periodic free vaccination.	20000 Animal	LSS		8,000			1000	1000	2000	3000	3000	2000	4000	4000		
Programme/Line deptt. Staff in animal reproduction, nutrition, livestock management	50 persons	LSS		4,166				10	10			10	10			
Deworming campaigns against contagious/infectious diseases & external and internal parasites.	20000 Animal	LSS		7,200			1000	1000	2000	3000	3000	2000	4000	4000		
b Distribution and demonstration:																
High yielding goats plus provision for vaccination, feed, quarantine	75 Goats	LSS		9,250								25	25	25		
Chickens of Fayoumi, Red Rhode/Golden Type among women for establishing backyard poultry farms	8640 Birds	LSS		24,644							200	500	800	600	540	

4. ANNUAL WORKPLAN 2007 (UNDP-GOB), Revised.

Key Activities	Target	Responsible Party	Budget Line	Estimated Cost (US\$)	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter		
					Jan.	Feb.	Mar.	Apr.	May	Jun.	Jul.	Aug.	Sep.	Oct.	Nov.	Dec.
Breed improvement through artificial insemination and natural mating.	6 bulls & 18 Rams	LSS		6,400								18	6			
Demonstration, fattening:		LSS														
a) Lamb kids.	600 Animal	LSS		2,000								50	50	450	50	
b) Calves.	30 Animal	LSS		820								10	10		10	
c) Ewe flushing.	2000 Animal	LSS		7,000								500	1000	500		
Veterinary kits to trained farmers/community workers	9 Kfts	LSS		2,600										9		
Demonstration plots for introduction of Alfa alfa/Napier/ Elephant grass, hybrid sorghum, Mot grass; Cost of seed, fertilizer, irrigator -37 units in 37 COs	30 Hectares	LSS		1,600				15	15							
Urea Molasses.	2000 UMB	LSS		3,000											1000	1000
Strengthen delivery of existing livestock dispensaries	11 Dispensaries	LSS		9,000				2	3			3				
Livestock specialist services				14,405												
Sub - Total Livestock				119,654												
3 Water Conservation and Management:																
a Physical Infrastructure																
Water harvesting & Spreading (Sailaba & Kushkaba Bandaat)	400 acre	NRM		38,000								50		100	100	50
Livestock water ponds	1 ponds	LSS		910										1		
Irrigation water Courses	34 schemes	WIS		151,700								4	5	5	5	5
Solar & Wind based irrigation system & solar lanterns	1 schemes	WIS		37,661										1		
Engineers services				20,985												
b Training:																
Stone Dressing/Pitching and Wire Weaving tech	60 persons	NRM		997										20		20
Junior Engineers,line Deptt. staff on designing/implementation of Infrastructure schemes.	10 persons	WIS		0					10							
Efficient use of water for irrigation	30 persons	WIS		950					10					10		10
Duty Travel Agt: Development				6,580												
Sub - Total Water Conservation and Management				257,784												
4 Skills Development Training																
Training:																
Embroidry and wool spinning for women	60 Person	SSS		3,500										75		100
Health hygiene and TBA	200 Persons	SSS		2,500					60					80		60
Sub - Total Skills Development Training				6,000												
5 Monitoring, Media and Publication:																
Promotional material		MAS		2,001												
Training Modules		MAS		2,000												
Workshops/seminars		MAS		2,000												
Radio Programs/TV/Documentaries		MAS		7,000												
Monitoring & Evaluation Specialist Services		M&E		14,405												
Media and Advocacy Specialist services		MAS		14,405												
Monitoring and Evaluation Assistant services		M&E		18,167												
GIS Assistant				9,884												
Duty Travel Technical Services				2,087												
Sub - Total Monitoring, Media and Publication				71,950												

4. ANNUAL WORKPLAN 2007 (UNDP-GOB), Revised.

Key Activities	Target	Responsible Party	Budget Line	Estimated Cost (US\$)	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter					
					Jan.	Feb.	Mar.	Apr.	May	Jun.	Jul.	Aug.	Sep.	Oct.	Nov.	Dec.			
SUB - TOTAL PROGRAMME COST				736,106															
PROGRAMME MANAGEMENT																			
6 Staff Salaries for Management and Support:																			
6.1 National Professionals																			
National Programme Coordinator				27,769															
Sr. Admin and Finance Officer				11,588															
6.2 Other Support Staff																			
Admin and Finance Assistants				18,172															
Other Support Staff				99,798															
Sub- Total Staff Salaries				157,328															
7 Equipments / O&M																			
7.1 Non-Expandable Equipments																			
Computers & Equipments				19,000															
7.2 Expandable Equipments/ O&M																			
O&M vehicle, office, utilitis, communication,stationary,sundries etc				109,553															
Sub-Total Equipments and O&M				128,553															
8 Premises																			
Office Rents & Security				17,454															
Sub-Total Premises				17,454															
9 Sundries																			
Duty Travel Programme Support				27,823															
Sub-TOTAL SUPPORT COST				348,525															
TOTAL PROGRAMME & SUPPORT COST				1,084,630															

5. ANNUAL WORKPLAN 2008 (UNDP-GOB)

Key Activities	Unit	Unit Cost (US\$)	Target	Responsible Party	Budget Line	Funding		Estimated Cost (US\$)	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			
						ADPB	WFP		Com	Jan.	Feb.	Mar.	Apr.	May	Jun.	Jul.	Aug.	Sep.	Oct.	Nov.	Dec.
1 Community Development:																					
1.1 CO Formation:																					
1.1.1	Community Development Supervisors services	3	360	SSS	71300	247,645	0	247,645													
1.1.2	Social Mobilizers services	36		SSS	71300	47,607		47,607													
1.1.3	Social Sector and Gender Specialist services	1		SSS	71300	171,705		171,705													
1.1.4	Duty Travel			SSS	71600	16,782		16,782													
1.2 Training:																					
1.2.1	CO office holders in CMST (two days each training)	Person	7 Training	SSS	63400	6,500	4,000	10,500													
1.3 Skill enhancement & small enterprise development trainings																					
1.3.1	Cutting & sewing training (15 days each training)	Women	69.18	SSS	63400	12,909	3,750	16,659													
1.3.2	Embroidery Training for women (15 days each training)	Women	75	SSS		1,584	1,875	3,459													
1.3.3	Display in exhibitions/visibility	Stall	250	SSS		5,625	1,875	7,500													
1.3.4	Awareness on Health & hygiene & Reproductive health	Women	35	SSS		500	-	500													
Sub - Total Community Development						267,054	7,750	274,804													
2 Agriculture Development																					
2.1 NRM (Crops Productivity and Rangeland Management):																					
a Training:																					
2.1.1	Training on water harvesting (watershed management)	Person	500	NRM	63400	475	1,625	2,100													
2.1.2	Nursery raising (training on almond and olive)	Person	100	NRM		375	1375	1,750													
b Distribution and Demonstration:																					
2.1.3	Plant Production (Almond and Olive)	Seedling	20000	NRM		100	250	350													
2.1.4	Planting of platable trees and shrubs on rangelands (Salt Bush).	Acres	80	NRM		1,000	1000	2,000													
2.1.5	Water harvesting & Spreading (Sallaba & Kushkaba Bandaat) PSI	Acres	142.5	NRM		1,333	2667	4,000													
2.1.6	NRM Specialist services		1	NRM	71300	44887	49888	21375													
Sub - Total Crops Productivity and Rangeland Management						63,188	10,280	94,843													
2.2 Livestock:																					
a Training and campaigns:																					
2.2.1	Community livestock extension workers development training (3 trainings for 30 days)	Person	320	LS	63400	27,524	1,500	30,690													
2.2.2	Improved rural poultry farming (50 Trainings for 2 days; 20 persons/training)	Person	0	LS		8,640	0	8,640													
2.2.3	Skill enhancement in sheep & goat raising and production (13 Trainings for 2 days; 20 persons/ training).	Person	0	LS		1,000	1250	2,250													
2.2.4	Periodic free vaccination+one day training of 1000 Herders	Animal	0.083/animal	LS		750	250	1,000													
2.2.5	Deworming campaigns against contagious/infectious diseases & external and internal parasites+one day training of 1000 Herders.	Animal	0.35/animal	LS		8300		8,300													
b Distribution and demonstration:																					
2.2.6	High yielding dairy goats for small enterprise development	Goat	125	LS	63400	46,683	0	52,913													
2.2.7	Rural poultry birds of Fayoumi/Red Rhode/Golden/cross type + feed among women for establishing backyard poultry farms (750 sets (12 birds/set)+750 bag feed).	Set	47	LS		10,625	1875	12,500													
2.2.8	Breed improvement natural mating a) Friesian bull	Bull	9	LS		21,150	2350	23,500													

5. ANNUAL WORKPLAN 2008 (UNDP-GOB)

Key Activities	Unit	Unit Cost (US\$)	Target	Responsible Party	Budget Line	Funding		Estimated Cost (US\$)	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			
						ADPB	WFP		Com	Jan.	Feb.	Mar.	Apr.	May	Jun.	Jul.	Aug.	Sep.	Oct.	Nov.	Dec.
2.2.9 b) Balochi, Hamal, Bavrigh, Rams/Bucks Demonstration, fattening:	Rams/Bucks	130	18	LS	63400	1,638	702	2,340	4	8	4	2									
a) Lamby/kids	Animal	3.5	200	LS		630	70	700		100	100	100									
c) Ewe/doe flushing	Animal	3.5	200	LS		630	70	700		100	100	100									
2.2.10 Veterinary kits to trained farmers/community workers (5 kits/district)	KIT	168	36	LS		6048	488	6,048	20	16	1500	2000									
2.2.11 Urea Molasses Blocks	Block	0.75	6500	LS		4,387		4,875		1000											
2.2.12 Livestock specialist services	1				71300	16,782		16,782													
Sub - Total Livestock						90,989	1,500	100,385													
2.3 Water Conservation and Management:																					
a Physical Infrastructure																					
2.3.1 Water supply schemes	Structures	3600	20	WIS	72100	212,100	56,700	384,000													
2.3.2 Water storage reservoir and channel lining	Structures	7700	30	WIS		50,400		72,000	5	5											
2.3.3 Rehabilitation of Karez (cleaning and Extension)	Schemes	5400	15	WIS		161,700		231,000	2	12	12	4									
b Training:																					
2.3.4 training on improved irrigation practices	Person	20	100	WIS	63400	2,000	0	2,000	20	40											
c Demonstration																					
2.3.5 High efficiency irrigation system	Plot	4500	10	WIS	63400	40,500	0	45,000													
2.3.6 Sr. Engineer Services	1				71300	16,782		16,782	2	3											
2.3.7 Jr. Engineer Services	3				71300	26,028		26,028													
2.3.8 Duty Travel					71600	4,340		4,340													
Sub - Total Water Conservation and Management						301,750	56,700	478,150													
3 Technical Services																					
3.1 Monitoring & Evaluation																					
a Survey & Studies																					
3.1.1 Baseline Survey	Survey	50000	1	M&E	63400	77,750	0	77,750													
3.1.2 Management Information System	MIS	25,250	1	M&E		45000		45000													
3.1.3 Operational Research/Outcome studies	Studies	5000	3	M&E		25,250		25,250													
3.1.4 Capacity building of M&E staff	Person	2500	4	M&E		5,000		5,000													
b M&E technical services																					
3.1.5 Monitoring and Evaluation Specialist Services	1				71300	16,782		16,782													
3.1.6 Monitoring and Evaluation Assistants services	3				71300	26,028		26,028													
Sub - Total Monitoring & Evaluation						120,560	0	120,560													
3.2 Media and Publication:																					
a Publication:																					
3.2.1 Publications/promotional material/ printings			Need based																		
3.2.2 PSI Signboards (ironboards, painting & writing)			100	MAS	74500	15,000	0	15,000													
3.2.3 Audio/Video documentaries				MAS		1,500		1,500													
3.2.4 MAS technical services				MAS		3,500		3,500													
3.2.5 Media and Publication Specialist services	1			MAS	71300	16,782		16,782													
GIS Assistant Services	1			M&E	71300	10,341		10,341													
Duty Travel					71600	2,532		2,532													
Sub - Total Media and Publication						44,655	0	44,655													
SUB - TOTAL PROGRAMME COST						888,196	76,230	1,113,397													
PROGRAMME MANAGEMENT																					
4 Staff Salaries for Management and Support:																					
4.1 National Professionals																					
National Programme Coordinator	1				71300	29,752		29,752													
Sr. Admin and Finance Officer	1					13,540		13,540													
Sub total National Professionals						43,292	0	43,292													

5. ANNUAL WORKPLAN 2008 (UNDP-GOB)

Key Activities	Unit	Unit Cost (US\$)	Target	Responsible Party	Budget Line	Funding			Estimated Cost (US\$)	1st Quarter			2nd Quarter			3rd Quarter			4th Quarter							
						ADPB	WFP	Com		Jan.	Feb.	Mar.	Apr.	May	Jun.	Jul.	Aug.	Sep.	Oct.	Nov.	Dec.					
4.2 Other Support Staff					71400																					
Admin and Finance Assistants	4					23,031			23,031																	
Other Support Staff						114,132			114,132																	
Sub- Total Support Staff						137,163	0	0	137,163																	
Duty Travel					71600				19,941																	
5 Equipments / O&M																										
5.1 Non-Expandable Equipments																										
Computer, furnitures & Equipments					72200	15,000			15,000																	
5.2 Expandable Equipments/ O&M																										
Rental & O&M equipments etc					73400	115,147			115,147																	
Miscellaneous (Utilities, stationary, communication, sundries etc)					74500	31,532			31,532																	
6 Premises																										
6.1 Rental, repair & security of premises					73100	29,274			29,274																	
SUB-TOTAL SUPPORT COST						991,349	0	0	991,349																	
TOTAL PROGRAMME & SUPPORT COST						1,279,545	76,230	148,971	1,504,746																	

Note:

WFP Denomination is about to be increased and the remaining amount shall be utilized under same activities.



Annexes

**AREA DEVELOPMENT PROGRAMME BALOCHISTAN PHASE - II
LIST OF COMMUNITY ORGANIZATIONS 2007**

S. No.	CO_ID	CO_Name	Date of Establishment	CO HH	Vilg. HH	Members	President	Manager	Saving
Kalat									
Female									
2	KT009	Chad Trasani	18-May-2007	20	26	20	Fatima	Kazbano	Rs.1,100
3	KT013	Jangi Zai	21-Jul-2007	26	30	26	Haneefa	Sazaain	Rs.330
4	KT014	Ralki Zai	17-Jul-2007	26	34	26	Zainab	Gul Jan	Rs.520
5	KT015	Roshan Abad 1	21-May-2007	15	17	15	Khair un Nisa	Hameeda	Rs.1,190
6	KT016	Roshan Abad 2	21-May-2007	22	23	16	Faiz Bibi	Bilkees	Rs.1,380
7	KT017	Budla	05-Jun-2007	24	28	24	Hajani	Zawer	Rs.720
8	KT018	Shori	12-Jun-2007	17	17	17	Kaz Bano	Hajira	Rs.340
9	KT019	Shakh Hussaini	24-May-2007	16	21	16	Saib Khatoon	Sun Naz	Rs.1,000
10	KT020	Mengal Abad 2	11-Jul-2007	17	21	17	Rabia	Zubaida	Rs.170
11	KT021	Jori Ralki Zai	17-Jul-2007	13	13	13	Gul Jan	Bibi Laki	Rs.130
12	KT022	Muhammad Zai	17-Jul-2007	26	33	26	Zaida	Sharaf Khatoon	Rs.480
13	KT011	Ghraeeb Abad	11-Jul-2007	20	24	20	Hajani Dur Khatoon	Fatima	Rs.285
14	KT012	Shori Mengal	12-Jun-2007	19	26	19	Bas Naz	Abida	Rs.380
15	KT010	Gamboola	24-May-2007	22	27	22	Sharaf Naz	Gul Khatoon	Rs.1,320
16	KT008	Mengal Abad	22-May-2007	21	21	21	Khadija	Noor Khatoon	Rs.600
17	KT029	Chad	26-Oct-2007	13	16	13	Zar Bakth	Asma	Rs.0
18	KT033	Killi Mengal	11-Aug-2007	27	30	27	Murad bibi	Mahbibi	Rs.0
19	KT034	Killi Sunnadi	30-Aug-2007	12	15	12	hidaya khatoon	fateh khatoon	Rs.0
20	KT035	Huddi zehri	11-Jul-2007	20	21	20	Taj bibi	Rehmat khatoon	Rs.0
21	KT038	Mir Hajji	30-Oct-2007	0	0	20	Sahib Khatoon	Mah Bibi	Rs.0
22	KT024	Mal Lashkari	13-Sep-2007	16	21	16	Shakar Bibi	Zulekha	Rs.0
Male									
23	KT007	Shori 1	20-Jun-2007	16	21	16	Muhammad Eassah	Nazir Ahmed	Rs.600
24	KT006	Roshan Abad	21-May-2007	28	38	28	Abdul Ghani	Hafiz Abdul Wahab	Rs.1,440
25	KT004	Chad Trasani	26-May-2007	21	27	21	Abdul Nasir	Nasrullah	Rs.1,000
26	KT003	Chad Shair Ali	26-May-2007	24	30	24	Maqbool Ahmed	Mohammad Anwer	Rs.1,500
27	KT002	Budla	05-Jun-2007	24	30	24	Nisar Ahmed	Haji Mohammad Hassan	Rs.900
28	KT001	Mengal Abad	04-Jun-2007	16	21	16	Haji Hazoor Bakshsh	Mohammad Alim	Rs.1,050
29	KT030	Bright future	19-Sep-2007	27	32	27	Abdul Rauf	Abdul Baqi	Rs.0
30	KT023	Hatyari 2	26-Oct-2007	16	23	16	NoorJan	Afzal	Rs.0
31	KT005	Chad Gamboola	28-May-2007	24	30	24	Shafi Mohammad	Abdul Ali	Rs.1,000
32	KT036	Mengal Abad 2	22-Aug-2007	20	21	20	Abdul Hakeem	Amir Bakshsh	Rs.0
33	KT031	sunnadi	28-Sep-2007	14	15	14	Abdul samad	karim bukshsh	Rs.0
34	KT037	killi Menagal	19-Aug-2007	27	36	27	Rah hussain	Fazal Mohd	Rs.0
35	KT028	Mengal society	15-Sep-2007	25	31	25	Immam dad	Gulam dastageer	Rs.0
36	KT027	Ghareeb Abad	23-Oct-2007	15	22	15	Hafiz Bashir	Lal Mohd	Rs.0
37	KT026	Hadi Zehri	13-Sep-2007	18	21	18	Ghulam Qadir	Ghulam Rasool	Rs.0
38	KT025	Chad	26-Oct-2007	14	16	14	NoorJan	Sarwar	Rs.0
39	KT032	Hatyari 1	28-Sep-2007	22	27	22	Mohd Rafiq	M Jan	Rs.0
Khuzdar									
Female									
40	KZ022	Aabi Noghay	02-Aug-2007	17	20	21	yasmeen	Parveen	Rs.340
41	KZ023	Killi Taj Muhammad	02-Aug-2007	17	32	23	Naseema	Khairunisa	Rs.1,020
42	KZ019	Jo Parko 1	25-May-2007	23	28	28	Gul Bibi	Ameena	Rs.6,100
43	KZ021	Ali Hassan Parko	11-Jun-2007	16	20	20	Haneefa	Sameena	Rs.2,400
44	KZ020	Marave Parko	21-May-2007	17	24	24	Naz Bibi	janmat Khatoon	Rs.3,200
45	KZ018	Bunap Parko	22-May-2007	18	21	22	Jan Bibi	Maryam	Rs.4,900
46	KZ017	Battar Parko	25-May-2007	22	24	24	Sheher Bano	Aamna	Rs.3,600
47	KZ024	Killi Jan Muhammad	31-Jul-2007	17	24	30	Rubeena	Rehmat Khatoon	Rs.1,020
48	KZ015	Ghaffarabad - II	19-May-2007	10	16	16	Ganj Khatoon	Bibi	Rs.1,200
49	KZ030	Chib Bajodi	18-Aug-2007	19	22	17	Zulikha	Khan Bibi	Rs.680
50	KZ014	Ghaffarabad - I	19-May-2007	20	22	22	Patani	Janat khatoon	Rs.2,400
51	KZ013	Peepali	22-May-2007	18	20	18	Hajra	Noor Bibi	Rs.2,240
52	KZ016	Jaori Parko	05-Jun-2007	10	15	15	Zubaida	Kaz Bano	Rs.1,000
53	KZ027	Darwazo	18-Sep-2007	15	21	20	Fatima	Fatima	Rs.0
54	KZ028	Shorai Jaori	20-Sep-2007	10	15	15	Raj bibi	Rogja	Rs.200
55	KZ029	Jo Parko 2	04-Sep-2007	22	25	25	Hseena	Farzana	Rs.2,600
56	KZ034	Choki Noghey1	01-Aug-2007	20	20	15	Zeenat	Shahbibi	Rs.900
57	KZ035	Choki Noghey2	01-Aug-2007	21	21	14	Safoora	Khadija	Rs.1,100
58	KZ012	Alangi	22-May-2007	16	22	22	Sumari	Khair Bibi	Rs.1,880
Male									
59	KZ008	JO Parko 1	25-May-2007	21	28	28	Nasser Ahmed	Suliman	Rs.3,350
60	KZ007	Bunap Parko	22-May-2007	16	21	22	Abdul Ghafoor	Mohammad Noor	Rs.5,760
61	KZ005	Jaori Parko	05-Jun-2007	12	15	15	Mohammad Amin	Imam Bakshsh	Rs.1,280
62	KZ004	Tahri Ithad J.A Peepali	22-May-2007	14	20	18	Abdul Qadeer	Mola Bakhash	Rs.1,680
63	KZ003	Alangi Parko	22-May-2007	16	22	22	Munir Ahmad	Mohammad Amin	Rs.4,700
64	KZ002	Ghaffarabad 2	19-May-2007	16	16	16	Mohammad Ismail	Hazoor Bakhash	Rs.4,800
65	KZ009	Marave Parko	21-May-2007	15	24	20	Attah ullah	Amanullah	Rs.3,600
66	KZ006	Battar Parko	25-May-2007	20	24	24	Mohammad Raheem	Manzoor Ahmed	Rs.6,350
67	KZ036	Killi Jan Muhammad	02-Aug-2007	24	24	17	Jan Mohammad	Abdul Nabi	Rs.1,740
68	KZ011	Killi Taj Muhammad	02-Aug-2007	27	32	32	Abdul Wahab	Abdullah	Rs.1,620
69	KZ038	Kalan Bajodi	26-Oct-2007	25	30	25	Haji Mohd Siddique	Jalil Ahmed	Rs.0
70	KZ010	Ali Hassan Parko	11-Jun-2007	16	20	20	Ali Hasan	Abdul Rasool	Rs.2,500
71	KZ037	CO JO Parko 2	19-Oct-2007	16	25	14	Muneer	Salam	Rs.1,000
72	KZ033	Choki Noghey2	06-Aug-2007	21	21	17	Rais AbdulHayee	Abdul Ghani	Rs.920
73	KZ032	Choki Noghey1	01-Aug-2007	20	20	14	Abdul Samad	Ghulam Hussain	Rs.840
74	KZ031	Chib Bajodi	02-Aug-2007	19	22	15	Ghulam Rasool	Noor Mohammad	Rs.1,000
75	KZ026	Shorai Jaori	20-Sep-2007	11	15	15	sanaullah	Abdul Hahy	Rs.240
76	KZ025	Darwazo	18-Sep-2007	15	21	20	Sahdullah	Abdullah	Rs.0
77	KZ001	Ghaffarabad 1	19-May-2007	16	22	22	Mohammad Karim	Abdul Wahid	Rs.4,500

**AREA DEVELOPMENT PROGRAMME BALOCHISTAN PHASE - II
LIST OF COMMUNITY ORGANIZATIONS 2007**

S. No.	CO_ID	CO_Name	Date of Establishment	CO HH	Vilg. HH	Members	President	Manager	Saving
Loralai									
Female									
78	LL035	Gul kach		13	14	9	mahai	badoo	
79	LL024	Bagazai	10-Nov-2007	16	15	16	feroza	malta	Rs.0
80	LL025	surkai sharan	14-Nov-2007	25	25	23	shabai	khan bibi	Rs.140
81	LL026	Sara qilla	29-Oct-2007	14	16	14	naik bukhta	ubash	Rs.130
82	LL033	ZAr sakhar 1		15	16	15	Atalasa	khawabai	
83	LL027	sanwased	27-Oct-2007	13	20	13	tajoo	dawlat	Rs.130
84	LL005	Aqrabai		18	18	18	tootai	Momina	Rs.250
85	LL032	zar sakhar 2		13	13	14	khan sura	balosa	
86	LL036	Gidawal balla 11		15	15	15	makhai	sahiboo	Rs.150
87	LL023	pasta khan	15-Nov-2007	15	15	13	Halima	Sabai	Rs.0
88	LL018	Nawarang Abad	11-Sep-2007	18	18	18	Kanal bibi	Gul bibi	Rs.0
89	LL019	Dawlot china	28-Sep-2007	15	15	15	Saido	Mandina	Rs.150
90	LL022	center gidawal	24-Oct-2007	14	14	15	Momina	Khambai	Rs.0
91	LL020	Gidwal bala	27-Sep-2007	15	18	17	wabai	kapai	Rs.170
92	LL021	nali malazai	20-Oct-2007	15	15	15	bukhai	sahiboo	Rs.320
93	LL034	Nali malazai 11		13	13	13	Bawata	khumaroo	
Male									
94	LL013	Nali walazai 1	18-Jul-2007	16	17	13	A.wasey	Hassan khan	Rs.500
95	LL014	Sarwazhad	30-May-2007	14	20	14	Mohad Essa	Abdul Wahab	Rs.2,500
96	LL028	malazai 2	06-Nov-2007	13	13	13	asad khan	taj uddin	Rs.1,120
97	LL001	Nawrang abad	24-May-2007	14	14	14	Norakhan	sobidar	Rs.1,240
98	LL012	center gidawal	14-Jun-2007	14	14	14	Rozai khan	Shair mohad	Rs.0
99	LL011	Sarkai sharan	12-Jun-2007	23	25	16	Salah u din	DR jamall	Rs.6,076
100	LL015	Gidwai bala	25-May-2007	16	16	12	Mir gul	Molvi Nazer M	Rs.3,200
101	LL010	Nali walazai 2	25-Jul-2007	20	20	16	Jalal u din	Mola jan	Rs.830
102	LL009	Dargai wath	16-Aug-2007	19	36	19	Mehdi	Dur mohad	Rs.1,300
103	LL008	Aqrabai	31-May-2007	18	18	16	M.Ramazan	Berhamat	Rs.20,550
104	LL007	Pasta khan	21-May-2007	14	15	14	Agha mohad	Afzal khan	Rs.2,220
105	LL006	Sara qilla	25-May-2007	14	16	14	A.Satar	Habib ullah	Rs.6,600
106	LL003	Ger sakhar	15-Jun-2007	11	16	11	Fazal mohad	Sultan	Rs.500
107	LL016	Nali Mulazai	18-Jul-2007	15	15	15	Nizamuddin	Abdul Khalq	Rs.950
108	LL031	Gul kach	09-Nov-2007	11	11	11	Habeeb ullah	surab khan	Rs.170
109	LL004	Bagazai	14-Jun-2007	13	15	13	Shahwazer	Dadkhan	Rs.100
110	LL002	Dawlat china	26-Jul-2007	12	15	12	Hazarat bilal	Mira shah	Rs.5,900
111	LL029	zar sakhar 2	19-Nov-2007	15	15	15	Baran khan	sudd.mir	Rs.0
112	LL030	Gidwai bala 2	24-Nov-2007	16	15	16	Hameed ullah	said ullah	Rs.2,520
113	LL017	Wasil	24-Sep-2007	12	18	12	Mohammad gul	shadi khan	Rs.600
Qila Saifullah									
Female									
114	Q5037	Idress Talari 2	22-Nov-2007	20	20	11	yasmeen	zalefa	Rs.285
115	Q5036	A.Samad karez	15-Nov-2007	12	16	12	Harifa	sajida	Rs.300
116	Q5020	Rahim gul Karez	17-Aug-2007	12	27	12	Maina	Arifa	Rs.12,005
117	Q5030	Asozai	11-Sep-2007	12	35	12	shahida	khalida	Rs.2,050
118	Q5029	Sur karez	18-Oct-2007	35	13	35	khalida	Amina	Rs.540
119	Q5028	Spin karez	03-Oct-2007	30	14	30	Sahira	Breshmina	Rs.475
120	Q5027	Sangar 2	05-Oct-2007	28	13	28	Rashida	Feroza	Rs.390
121	Q5012	Lalozai Karez	30-May-2007	10	25	10	Amina	Sajida	Rs.3,760
122	Q5022	Sangar 1	19-Sep-2007	15	15	15	Rofiza	Hasia	Rs.910
123	Q5013	New Lalozai karez	13-Jun-2007	10	25	11	Hanifa	Amina	Rs.3,510
124	Q5019	Makhai Karez	14-Jun-2007	14	34	15	Hanifa	Fatima	Rs.3,270
125	Q5018	Takai Karez	06-Jul-2007	12	17	13	Sardar Bilbi	Robina	Rs.2,240
126	Q5017	Zaghloona M. Jan II	02-Jul-2007	12	10	12	Qasima	Khalida	Rs.2,470
127	Q5016	Yaqoob Karez	08-Jun-2007	10	35	10	Hajira	Marum	Rs.58,750
128	Q5015	Idress Talari	31-Aug-2007	10	50	10	Khatima	Fatima	Rs.1,080
129	Q5014	Zaghloona M. Jan	30-May-2007	10	50	10	Foudina	Zarsangha	Rs.3,800
130	Q5023	surkai karez	28-Sep-2007	13	13	13	Khalida	Ammina	Rs.720
Male									
131	Q5040	Aollazai		15	15	15	shams ullah	H.Ghulam .M	
132	Q5039	Chishinkai		16	16	16	shair Mohammad	Zain Ullah	
133	Q5008	Makhai Karez	24-Jul-2007	18	80	18	Zain Ullah	Shahab Din	Rs.180,000
134	Q5033	Asozai	10-Nov-2007	25	25	17	allah noor	A.Mateen	Rs.500
135	Q5032	abdul samad karez	15-Nov-2007	16	16	16	H.Amir Mohammad	M.A.Samad	Rs.300
136	Q5031	sangar 1	13-Nov-2007	35	35	24	abdul majeed	jan mohammad	Rs.500
137	Q5026	Warjooraba	18-Oct-2007	20	18	18	Sardar Mohad	M.noor	Rs.500
138	Q5025	Sur karez	19-Oct-2007	16	16	16	Ahemad jan	M.noor	Rs.500
139	Q5024	Yaqoob Karez		16	16	16	Abdul Mateen	Roh ullah	Rs.500
140	Q5021	surkai karez	28-Sep-2007	16	16	16	kalim ullah	khudia Rahem	Rs.300
141	Q5011	Kam Ranzai karez	17-Jul-2007	18	28	18	Mohib Ullah	Zain Ullah	Rs.23,049
142	Q5009	Rahim gul Karez	25-Jul-2007	16	27	16	Ehsan Ullah	Asmath Ullah	Rs.56,403
143	Q5034	khusaya	27-Nov-2007	15	16	15	M.Akbar	Allah u ddin	Rs.300
144	Q5007	Marpal II	21-Aug-2007	15	19	6	A. Qahir	Zahir Khan	Rs.2,700
145	Q5006	Marpal I	21-Aug-2007	15	17	8	Sado Khan	M. Khan	Rs.3,500
146	Q5005	Ali Ghat	15-Jun-2007	20	45	8	Aibath Khan	Ali Shah	Rs.11,300
147	Q5004	Idress Talari	08-Jun-2007	17	42	16	M. Anwar	Shams Ullah	Rs.42,530
148	Q5003	Zaghloona M. Jan	31-May-2007	18	50	9	Haji M. Essa	M. Akbar	Rs.14,600
149	Q5002	New Lalozai karez	12-Jun-2007	15	40	10	A. Ghafoor	M. Ashrif	Rs.16,200
150	Q5001	Lalozai Karez	31-May-2007	15	25	10	Kamal Khan	Rozza Din	Rs.16,100
151	Q5035	Ubashtai	23-Nov-2007	15	25	15	Agha Mohammad	Aziz ul haq	Rs.300
152	Q5038	Taran shala		16	16	16	Munir ahmad	H.A.Rahim	
153	Q5010	Yaqooba	18-Jul-2007	15	25	15	A. Nasir	Naik Mohd	Rs.13,125

**AREA DEVELOPMENT PROGRAMME BALOCHISTAN PHASE - II
LIST OF COMMUNITY ORGANIZATIONS 2007**

S. No.	CO_ID	CO_Name	Date of Establishment	CO HH	Vilg. HH	Members	President	Manager	Saving
Ziarat									
Female									
154	ZT039	Saido aghberg	12-Nov-2007	17	17	17	Bibi Hilal	Danista	Rs.0
155	ZT022	Shirin pitao	13-Jun-2007	12	16	12	Zardana	Gulbai	Rs.380
156	ZT032	New poi adha	25-Jul-2007	30	30	30	Abida	Hidaya	Rs.2,090
157	ZT020	Lal mohad	24-May-2007	15	20	15	Fatima	Rozina	Rs.400
158	ZT021	Ghabergai	15-Jun-2007	10	15	10	koter bibi	zarina	Rs.280
159	ZT023	Gangale	15-Jun-2007	10	13	10	Balkisa	Bukhat bibi	Rs.0
160	ZT024	Ghabergai amanullah	29-Jun-2007	10	15	10	Bukhtavi	Rostai	Rs.300
161	ZT025	Ghundan	29-May-2007	12	15	12	Bukhat nama	Dolot bibi	Rs.0
162	ZT026	Garvash	24-May-2007	19	21	19	Khadija	Nazai	Rs.280
163	ZT027	Shahzai	15-Jun-2007	12	13	12	Siraj bibi	Bukhtnama	Rs.480
164	ZT028	Salo landai	25-Jul-2007	11	15	11	Zardana	jan bukhat	Rs.290
165	ZT029	Shah khuz	28-Jul-2007	12	20	12	Bukhtori	jamal bibi	Rs.300
166	ZT019	Saeed abad	29-May-2007	15	16	15	Amna	jamila	Rs.300
167	ZT031	Poi adha	25-Jul-2007	20	20	20	Amna bibi	Akhterbai	Rs.1,020
168	ZT018	Anghashai	06-May-2007	21	25	21	Zainai	Akhter bibi	Rs.0
169	ZT033	Marghaloona	30-Aug-2007	12	18	12	Marium	Bibi hamida	Rs.190
170	ZT030	Hassan abad	25-Jul-2007	20	20	20	Nor bibi	Zubiada	Rs.390
Male									
171	ZT016	Ghabergai aman u ilah	23-Jun-2007	15	15	15	Aman ullah	Mohad khan	Rs.1,030
172	ZT015	Gangale	12-May-2007	13	13	13	M ramazan	abdul aziz	Rs.0
173	ZT014	shah khuz	21-Jul-2007	20	20	20	M. baz mohad	M.nazar	Rs.1,030
174	ZT013	Ghundan	29-May-2007	15	18	15	abdul malik	Zahir	Rs.0
175	ZT012	Angashai	16-Jun-2007	25	25	25	khanai	Mohad rahim	Rs.0
176	ZT040	Gharmak new killi		19	19	19	abdul wahab	abdul ghani	
177	ZT011	Saido aghberg	28-Jul-2007	17	17	17	Mohad raza	Mohad amin	Rs.0
178	ZT038	Mazzai	14-Nov-2007	17	17	17	M.Yousaf	A.Majeed	Rs.0
179	ZT017	Shalzai	13-Jun-2007	13	13	13	Abdullah khan	Baz mohad	Rs.1,030
180	ZT037	Shirin sierkai	18-Nov-2007	16	16	16	Hafez Gula khan	shikar khan	Rs.0
181	ZT036	Sierkai	26-Oct-2007	15	30	16	M.Amin	M.Hashim	Rs.0
182	ZT008	Ghabergai	15-May-2007	13	15	13	zardad	khan mohad	Rs.0
183	ZT035	Toor dag	21-Oct-2007	14	20	14	M.raza	H.Bilal	Rs.0
184	ZT007	New poi adha	08-Aug-2007	20	30	20	shah mohad	Bahi khan	Rs.1,030
185	ZT006	Hassan abad	27-Jul-2007	17	23	17	zardad	Ahmad noor	Rs.1,030
186	ZT005	Salo landai	25-Jul-2007	13	15	13	rozay mohad	khair mohad	Rs.1,030
187	ZT004	shirin pitao	30-May-2007	16	16	16	saeed ahmad	Din mohammad	Rs.1,030
188	ZT003	Garvesh	11-Jun-2007	13	21	13	Noroz shah	Amir mohad	Rs.0
189	ZT002	Saeed abad	29-May-2007	15	20	15	salah u din	abdul salam	Rs.1,030
190	ZT001	Molvi lal Mohammad	24-May-2007	13	20	13	Molvi lal M	Wazir M	Rs.1,030
191	ZT010	poi adha	12-Jul-2007	20	20	20	asad khan	Mohad noor	Rs.1,030
192	ZT009	Marghloon	30-Aug-2007	18	18	18	abdul waris	shah mohad	Rs.0
193	ZT034	Kandara		15	20	15	khalid khan	Asmat ullah	Rs.500
Mastung									
Female									
194	MT032	Jarzal-2				18			Rs.0
195	MT040	Gul e Lal	10-Nov-2007	21	70	32	Haleema	Shams Khatoon	Rs.0
196	MT039	Shaheen	06-Nov-2007	15	70	18	Zubaida	Fatima	Rs.0
197	MT021	Gulab zai (Moqaddus)	25-May-2007	18	38	18	safia	Razima	Rs.2,360
198	MT033	Ash Khan (Chambelli)							Rs.0
199	MT031	Sumarzal-1				15			Rs.500
200	MT030	Faqirzai				15			Rs.500
201	MT029	Jarzal-1				14			Rs.500
202	MT028	Bashamzai				18			Rs.625
203	MT027	Ash Khan (Sitara)	25-Sep-2007	20	24	18	Noor Jan	Giul Jamal	Rs.0
204	MT026	Ash Khan (Gulab)	11-Sep-2007	18	18	17	zarina	Abida	Rs.300
205	MT025	Notak Zai (Kanwal)	20-Aug-2007	17	60	17	Hakim Zadi	Safora	Rs.1,205
206	MT024	Sawal Khan Zai (Karan)	23-Jul-2007	20	20	21	Asia	Tahira	Rs.4,600
207	MT023	Sammur Zai (Roshini)	29-May-2007	18	60	18	Sher bibi	Nil	Rs.1,860
208	MT022	Syed zai (sadat)	28-May-2007	18	16	20	Aziz Bakht	Fouzia	Rs.2,800
209	MT034	Ashkan-1							Rs.0
Male									
210	MT003	Kirdgap Development	29-May-2007	17	20	17	Nasir Ahmad	Sultan all	Rs.2,500
211	MT014	Alfalsh Development	26-May-2007	17	34	17	Abdul Ghafar	Qadir Bux	Rs.2,500
212	MT042	Abad-2 Dev. Society	15-Nov-2007	15	70	15	Saeed Ahmed	Ayub Shah	Rs.500
213	MT041	Game Dev. Society	15-Nov-2007	25	25	15	Rasool Baksh	Khair Muhammad	Rs.500
214	MT038	Killi Zakria - 2	23-Oct-2007	21	70	15	Ataullah	Habibur Rehman	Rs.0
215	MT037	Killi Zakria - 1	23-Oct-2007	21	70	15	Dost Muhammad	Naseer Ahmed	Rs.0
216	MT036	Killi Musa - 2	23-Oct-2007	22	170	15	Abdul Raziq	Abdul Malik	Rs.0
217	MT035	Killi Musa - 1	23-Oct-2007	22	170	15	Shah Faisal	Ataullah	Rs.0
218	MT020	South Kirdgap Development	22-Aug-2007	18	130	18	Abdullah	Jamil ahmed	Rs.1,000
219	MT019	Al-Khair development	22-Aug-2007	19	100	19	Khan Muhammad	Behdar Khan	Rs.1,000
220	MT018	Shahnawaz Development	21-Aug-2007	15	40	15	Ramatullah	Muhammad Abas	Rs.1,000
221	MT017	Sarpra Development Society	21-Aug-2007	23	30	23	Imam Bux	Pervaz Ahmed	Rs.1,000
222	MT001	Development Conscious	28-May-2007	22	28	22	Mumtaz Ahmad	peer Jan	Rs.2,500
223	MT015	Hairaf Development	29-May-2007	21	30	21	Barkat Ali	Mumtaz Ahmad	Rs.2,500
224	MT002	Zamandar Development	28-May-2007	22	32	25	Abdul Hai	Nabi Bux	Rs.2,500
225	MT013	Rage Development	26-May-2007	17	25	17	Saefer Ahmed	Ishtaq Ahmad	Rs.1,700
226	MT012	Syed Development	29-May-2007	17	25	15	Ghulam Fatah shah	Shams-ul-haq	Rs.2,500

**AREA DEVELOPMENT PROGRAMME BALOCHISTAN PHASE - II
LIST OF COMMUNITY ORGANIZATIONS 2007**

S. No.	CO_ID	CO_Name	Date of Establishment	CO HH	Vilg. HH	Members	President	Manager	Saving
227	MT011	Mahaar Development	29-May-2007	27	35	18	sajjad	Amjad Ali	Rs.2,000
228	MT010	Goarakh Society Kirdgap	21-Aug-2007	17	100	14	Khalil Ahmed	Gul Hassan	Rs.1,000
229	MT009	Asad abad society	21-Aug-2007	17	35	17	Abdul Baqi	Meer Ahmed	Rs.1,000
230	MT008	Abad society	22-Aug-2007	17	70	17	Muhammad Waris	Muhammad Ismail	Rs.1,000
231	MT007	Al- Khidmat Development	22-Aug-2007	21	100	21	Abdul Malik	Muhammad yousaf	Rs.1,000
232	MT006	Gharibabad development	28-May-2007	25	30	25	Muhammad Noor	Fazal Khan	Rs.2,500
233	MT005	Astar Development	28-May-2007	25	25	22	Javad Ahmad	Abdul Malik	Rs.2,500
234	MT004	Developers society	29-May-2007	22	25	22	Tariq Ahmad	Waqar Ahmad	Rs.2,500
235	MT016	Shahdade Development	26-May-2007	17	35	17	Imtaz Ahmad	Jahanzab	Rs.2,500
Pishin									
Female									
236	PN023	Siwgi durgai	29-May-2007	9	14	9	Haleema	Bakhtnama	Rs.1,520
237	PN043	Murgha Zakriazai-2	16-Nov-2007	14	50	14	Bala Nasta	Nazira	Rs.0
238	PN042	Murgha Zakriazai-1	16-Nov-2007	15	55	15	Gul Badan	Maira Khan	Rs.0
239	PN037	Lumar Baloch	21-Oct-2007	10	15	12	Bibi Shafia	Mamai	Rs.600
240	PN030	Gajai							Rs.120
241	PN036	Kooz Baloch	20-Oct-2007	10	15	11	Saira	Sakhula	Rs.400
242	PN028	Jane Alka	26-Sep-2007	10	12	10	Hajra	Shafia	Rs.150
243	PN016	Kooz Obashtgai	24-May-2007	12	20	12	Sakhula	Sesai	Rs.3,082
244	PN022	Thokhai nozai	16-Jun-2007	12	13	12	Tothya	Zubeda	Rs.270
245	PN021	Ghara Wolang	29-Aug-2007	14	15	14	Sadla	Gul seema	Rs.420
246	PN020	Walong	23-Aug-2007	10	12	10	Khateja	Malooka	Rs.390
247	PN019	Kooz Jhalak	26-May-2007	13	14	13	Mahmoora	Bakhtnama	Rs.1,460
248	PN018	Bala jahlak	26-May-2007	15	15	15	Naik Murgha	Poodina	Rs.1,600
249	PN017	Bala Obashtgai	24-May-2007	15	15	15	Noor bibi	Zubeda	Rs.2,650
250	PN029	Muzhvai	26-Sep-2007	10	15	10	Bibi Qafiya	Bibi Sara	Rs.200
Male									
251	PN003	Kooz Jhalak	26-May-2007	13	13	13	M. Hassan	Juma khan	Rs.2,770
252	PN004	Lower Jhalak	26-May-2007	15	15	15	Boor Mohd.	Zainullah	Rs.3,050
253	PN026	Lowar Ghabergai	25-Sep-2007	15	15	15	Aman Ullah	Khaliq Dad	Rs.750
254	PN027	Shas Muhammadzai	29-Sep-2007	20	20	20	Abdul Rahman	Mohd. Shah	Rs.2,000
255	PN031	Murgha Zakriazia-2	22-Oct-2007	27	50	11	Shams Kakar	Sahkoor Ahmed	Rs.0
256	PN010	Koz Shakh	25-Jul-2007	13	13	13	Abdul Karim	Juma khan	Rs.960
257	PN025	Khuja Zawar	25-Sep-2007	12	12	12	Naqeeb Ullah	M.Rahmatullah	Rs.600
258	PN024	Toor Tangi	25-Sep-2007	12	12	12	Abdul Shakoor	Faizul Haq	Rs.600
259	PN015	Gajai	16-Aug-2007	12	12	12	M. Essa	Shams ullah	Rs.550
260	PN001	Kooz Obestkai	24-May-2007	18	18	18	M. Yousaf	Amir jan	Rs.3,580
261	PN014	Tokai Nozai	16-Aug-2007	13	13	13	Abdul hakim	Nazirahmad	Rs.850
262	PN013	Shasa Smalzai	27-Aug-2007	23	23	23	Murad khan	M. Haq	Rs.1,460
263	PN012	Lower Baloch	27-Aug-2007	12	12	12	Bismillah	Salih Mohd.	Rs.740
264	PN011	Koz Baloch	27-Aug-2007	16	16	16	Abdul Malik	Niyamat ullah	Rs.1,120
265	PN002	Lower Obestkai	24-May-2007	15	15	15	Nasurullah	Zahir Shah	Rs.5,150
266	PN009	Wolang Ghara	02-Aug-2007	13	13	13	Muhalb ullah	Saif ullah	Rs.870
267	PN041	Mew Karez Maghribi	17-Nov-2007	14	14	14			Rs.0
268	PN040	Ziaba	17-Nov-2007	13	13	13			Rs.0
269	PN039	Baghdad	10-Nov-2007	11	11	11			Rs.0
270	PN038	Sparavoon	10-Nov-2007	12	12	12	Abdul Ghaffar	Faizul Haq	Rs.0
271	PN035	Western Churmian	24-Oct-2007	22	43	12	Bismillah	Muhammad Sadiq	Rs.0
272	PN034	Ragha Barakzai	24-Oct-2007	11	11	15	Abdul Rehman	Bahadur Khan	Rs.0
273	PN032	Murgha Zakriazia-1	22-Oct-2007	11	50	14	Muhammad Rafiq	Muhammad Anwer	Rs.1,000
274	PN008	Wolang	13-Jun-2007	13	13	13	Abdul karim	Dost mohd.	Rs.3,960
275	PN007	Soogai Dargai	29-May-2007	14	14	14	Abdul Aziz	Nazirahmad	Rs.3,190
276	PN006	Jane Alka	29-May-2007	14	14	14	M. kabir	M. Yousaf	Rs.1,400
277	PN005	Mouzai	29-May-2007	13	13	13	Dad ullah	Umai khan	Rs.4,550
278	PN033	Eastern Churmian	24-Oct-2007	35	50	16	Shamsuddin	Abdul Khalik	Rs.0
Quetta									
Female									
279	QT025	Killi Abdul Raheem	23-Aug-2007	20	20	20	Mahira	Raj bibi	Rs. 700
280	QT042	Kamil	21-Nov-2007	16	25	16	Salma	Zareena	Rs. 200
281	QT041	Momina	20-Nov-2007	19	25	19	Zakira	Taj Bibi	Rs. 0
282	QT032	Damanzai Roshaan	26-Sep-2007	17	30	17	Khalida	Bakhtawar	Rs. 100
283	QT019	Khanezai	07-Aug-2007	15	30	15	Sadiqa	Razia	Rs. 900
284	QT010	Killi Bungul Stara	25-May-2007	28	30	25	Haleema	Ruksana	Rs. 1980
285	QT011	Killi Gabezal 1 Lamer	24-May-2007	16	60	19	Zaba	Bibi Noor	Rs. 4840
286	QT012	Abdul Nabi (Gulab)	09-May-2007	19	25	19	Dur Bibi	Noor Khatoon	Rs. 1550
287	QT013	Khushbo Mehrabzai-2	25-Jul-2007	20	30	20	Bakhtawar	Razam	Rs. 690
288	QT014	Ujala Mehrabzai-3	23-Aug-2007	23	30	23	Zakhira	Sakeena	Rs. 260
289	QT015	Chambali Killi Anyat	28-Aug-2007	20	22	20	Sharif Naz	Zareena	Rs. 600
290	QT016	Killi Serwer	24-May-2007	14	15	14	Shafeea	Fouzia	Rs. 2100
291	QT027	Barozai	27-May-2007	17	30	17	Bibi Majbeen	Sapheea	Rs. 170
292	QT018	New Khalozai	25-May-2007	18	18	18	Ram Bibi	Gul Naz	Rs. 2590
293	QT031	Killi Ragi	20-Sep-2007	21	26	21	Sadoozal	Shakara	Rs. 1000
294	QT020	Mehrabzai-1	23-Aug-2007	16	20	16	Gulsika	Hajra	Rs. 600
295	QT021	Babozai-2	23-Aug-2007	20	25	20	Jamila	Asyah	Rs. 900
296	QT022	Sanjedi	27-May-2007	21	23	21	Bibi Parween	Bibi Hoor	Rs. 1050
297	QT023	Khounitalab	22-May-2007	20	25	20	Khair Bibi	Sadia	Rs. 1020
298	QT024	Killi Abdul Ali	31-May-2007	20	20	20	Hoor Bibi	Rahseeda bibi	Rs. 820
299	QT034	Ghabezai-2 (Sahar)	26-Oct-2007	20	63	20	Bibi Hameeda	Kafia Bibi	Rs. 2000
300	QT026	Babozai	23-Aug-2007	15	25	15	Aleema Bibi	Bibi Sarfia	Rs. 450
301	QT017	Abdizai	22-May-2007	18	20	18	Bibi Ruksana	Yasmeen	Rs. 450
								Zareena	Rs. 3240

Status of Water Harvesting Structures

Activity	Area coverage	Number of Schemes	Valley	Community	District
Water harvesting structures	70	7	Parco	1. Alangi , 2. tahir itiahadpipli 3. Ghaffarabad i, 4. Ghaffarabad ii 5. Jori , 6. Banf, 7. Battar ,	Khuzder
Water harvesting structures	20	2	Totak	1. Chaki Noug i 2. Chachki Noug i ii	
Wate harvesting structures	20	2	Gidder	1. Roshan abad, 2. Huddi zehri	Kalat
Wate harvesting structures	20	2	Aghbarg	1. Damanzai 2. Ghabzai	Quetta
Wate harvesting structures	20	2	Mekhtar	1. Giddawa balla , 2. Aqrabi	Loralai
Wate harvesting structures	80	8	Kirdgab	1. Gorakh, 2. sarpra, 3. shawnawz, 4. abad society 5. mathare, 6. asadabad, 7. al khair development, 8. al khadmat	Mustung
Water harvesting structures	90	9	Kirdgab	1. Welfare, 2. zamindar , 3. Gharibabad, 4. Alflah , 5. istar , 6. gardgab 7. Haraaf , 8. Syed, 9. Conscious promoter	

PROFILE OF BREEDING BULLS' COMMUNITY ORGANIZATION (FARMERS) IN ADPB VALLEYS 2007

S.No	Name of Farmer Father's Name	Name of CO	District	Valley	Tag No.	Address	Name of SM	CNIC No
1	Mera Gul S/O Haji Fateh Gul	Gidawal Bala	Loralai	Nali Azam	4	Village Kgidawal Bala, Nali Azam Valley, Tehsil Mekhtar, District Loralai	Muhammad Farooq	56302-6051315-5
2	Abdul Nabi S/O Sher Muhammad	Sanari (Sanadi)	Kalat	Giddar-1	5	Village Sanadi, UC Hathyari, Tesil surab, District Kalat, Tel. No. 0844- 602003	Nihal Khan	51202-1787266-5
3	Haji Amanullah S/OHaji Malik Mubarak Khan	Abdulzai	Quetta	Aghbargh	5686	Gali/Street Abdulzai, Aghbargh, UC-63 Quetta Tel. 081-2015355	Muhammad Iqbal	54400-0411049-1
4	Amnaullah S/O Mekhtar	Makhi Kareez	Killa Saifullah	Surri	98	Village Makhi Kareez, UC Kan Metharzai, Tehsil Muslim Bagh, District Killa Saifullah	Ehsanullah	56202-2805955-3
5	Naik Muhammad S/O Jan Muhammad	Sherin Pitaw	Ziarat	Poi	3	Village Sherin Pitaw, UC Choutair, Tehsil Sinjavi, District Ziarat	Gul Rang Zaib	55402-1562731-5
6	Ghulam Hussain S/O Sardar Ghulam Haider Khan	Kirdgap	Mastung	Kirdgap	100	Village Kirdgap, UC Kirdgap, Tehsil Kirdgap, District Mastung	Sarfraz Khan	51602-1122922-3

PROFILE OF BREEDING RAMS' COMMUNITY ORGANIZATION (FARMERS) IN ADPB VALLEYS 2007

S. No	Name of Farmer	Father's Name	Name of CO	Name of District	Name of Valley	Ram Tag No	Address	Name of SM	CNIC No
1	Said Muhammad (Lando)	Nazak	Sarwazd	Loralai	Nali Azam	62	Village Sarwazd, Nali Azam Valley, Tehsil Mekhtar, District Loralai	Muhammad Farooq	609-49-179775
2	Jamal Khan	Haji Payo Khan	Sirkhi Sharan	Loralai	Nali Azam	24	Village Sirkhi Sharan, Nali Azam Valley, Tehsil Mekhtar, District Loralai	Muhammad Farooq	56302-7652907-1
3	Hameedullah	Haji Sada Gul	Gidawal Bala-2	Loralai	Nali Azam	79	Village Gidawal Bala-2, Nali Azam Valley, Tehsil Mekhtar, District Loralai	Muhammad Farooq	56302-0827498-3
4	Alam Khan	Malik Maash	Nali Malazai	Loralai	Nali Azam	17	Village Nali Malazai, Nali Azam Valley, Tehsil Mekhtar, District Loralai	Najeeb Shah	56302-0834945-3
5	Muhammad Rafiq	Malik Muhammad Jan	Khuni Talab	Quetta	Aghbargh	80	Village Khuni Talab, UC Aghbargh, Tehsil and District Quetta	Muhammad Iqbal	54400-0412236-7
6	Ghulam Sarwar	Ghous Bakhsh	Abdul Nabi	Quetta	Aghbargh	89	Village Abdul Nabi, UC Aghbargh, Tehsil and District Quetta	Muhammad Iqbal	54400-0531727-1
7	Abdul Baqi	Said Muhammad	Babozai	Quetta	Aghbargh	52	Village Babozai, UC Aghbargh, Tehsil and District Quetta	Amir Khan	54400-156769-3
8	Abdul Qayum	Malik Ghulam Mohiudin	Ghaibzai	Quetta	Aghbargh	59	Village Ghaibzai, UC Aghbargh, Tehsil and District Quetta	Muhammad Iqbal	54400-7573982-1
9	Kamal Khan	Abdul Razzaq	New Lalozai	Killa Saifullah	Surri	61	Village New Lalozai Kareez, UC Kan Metharzai, Tehsil Muslim Bagh, District Killa Saifullah	Ehsanullah	56202-0952491-1
10	Rozi Din	Kalam Khan	Lalozai Kareez	Killa Saifullah	Surri	100	Village Lalozai Kareez, UC Kan Metharzai, Tehsil Muslim Bagh, District Killa Saifullah	Ehsanullah	56202-8411329-1
11	Naseebullah	Haji Abdul Hanan	Ali Ghat	Killa Saifullah	Surri	28	Village Ali Ghat, UC Kan Metharzai, Tehsil Muslim Bagh, District Killa Saifullah	Ehsanullah	56202-0956911-3
12	Muhammad Hussain	Khalo Khan	Idrees Talari	Killa Saifullah	Surri	47	Village Idrees Talari, UC Kan Metharzai, Tehsil Muslim Bagh, District Killa Saifullah	Ehsanullah	56202-0957021-9
13	Muhammad Raza	Bagar	Toor Dak	Ziarat	Poi	18	Village Toor Dak, UC Poi, Tehsil Sanjavi, District Ziarat	Gul Rang Zaib	55402-4797993-5
14	Baz Muhammad/Hafiz Gula Khan	Mulla Khuda I Dad	Shaizai	Ziarat	Poi	95	Village Shaizai, UC Poi, Tehsil Sanjavi, District Ziarat	Gul Rang Zaib	55402-2075852-3
15	Asad Khan	Samand Khan	Poi Ada	Ziarat	Poi	3	Village Poi Ada, UC Poi, Tehsil Sanjavi, District Ziarat	Gul Rang Zaib	55402-2861128-1
16	Din Muhammad	Sahib Khan	Sherin Pitaw	Ziarat	Poi	23	Village Sherin Pitaw, UC Poi, Tehsil Sanjavi, District Ziarat	Gul Rang Zaib	609-53-167607

Annex - 3b

17	Syed Maroof Shah	Syed Abdullah Shah	Gwarakh	Mastung	Kirdgap	2	Village Asadabad, UC Kirdgap, Tehsil and District Mastung	Hashnain	51602-2076148-3
18	Khan Muhammad	Lal Muhammad	Ash Khan (Al-Khair)	Mastung	Kirdgap	63	Village Ash Khan, UC Kirdgap, Tehsil and District Mastung	Sarfraz	51602-2218144-9
19	Manzoor Ahmed	Haji Shah Muhammad	Asadabad	Mastung	Kirdgap	4	Village Asadabad, UC Kirdgap, Tehsil and District Mastung	Hashnain	51602-0488341-7
20	Ubaidullah	Faizullah	Kirdgap Junibi	Mastung	Kirdgap	13	Village Kirdgap Junibi, UC Kirdgap, Tehsil and District Mastung	Srafaraz	51602-151665-9
21	Mhammad Rahim	Khuda Bakhsh	Battar	Khuzdar	Parko	87	Village Battar, UC Parko, Tehsil and District Khuzdar Tel. 848.704321	Fateh Muhammad	51401-0161462-3
22	Ghulam Sarwer	Bhai Khan	JO Parko 2	Khuzdar	Parko	60	Village Jo Parko, UC Parko, Tehsil and District Khuzdar Tel. 848.703035	Fateh Muhammad	51401-4837410-9
23	Hazoor Bakhsh	Khuda Bakhsh	Ghaffar abad II	Khuzdar	Parko	74	Village Ghafarabad-2, UC Parko, Tehsil and District Khuzdar	Muhammad Iqbal	51401-5310839-9
24	Abdul Jalil	Abdu Rahim	Alangi	Khuzdar	Parko	11	Village Alangi, UC Parko, Tehsil and District Khuzdar	Muhammad Iqbal	5140-29121710-0
25	Abdul Haleem	Shadi Khan	Mengalabad-2	Kalat	Giddar-1	90	Village Mengalabad-2, Chad Sher Ali, UC Hathary, Giddar, Tegsil Surab, District Kalat	Shah Nawaz	51202-1788888-3
26	Eid Muhammad	Muhammad Yousaf	Hathary-2	Kalat	Giddar-1	24	Village Hathary-2, UC Hathary, Giddar, Tehsil Surab, District Kalat, Tel. No. 03073839985	Nihal Khan	51202-1788510-7
27	Muhammad Rafiq	Karim Bakhsh	Hathary-1	Kalat	Giddar-1	58	Village Hathary-1, UC Hathary, Giddar, Tegsil Surab, District Kalat, Tel. No. 0844-442150	Nihal Khan	51202-4592327-3
28	Ghulam Dastagir	Muhammad Rafiq	Rekizai	Kalat	Giddar-1	68	Village Rekizai, UC Hathary, Giddar, Tegsil Surab, District Kalat, Tel. No. 0844-442121	Nihal Khan	51202-5966451-5
29	Abdul Karim (Hedayatullah)	Faiz Muhammad	Wolong Ghara	Pishin	Dilsora	16	Village Wolong Ghara, UC Dilsora, Tehsil Karezat, District Pishin	Allah Noor	54302-062622632-3
30	Jalaluddin	Khan Muhammad	Murgha Zakryazai	Pishin	Dilsora	36	Village Murgha Zakryazai, UC Dilsora, Tehsil Karezat, District Pishin	Allah Noor	54302-0291996-5
31	Abdul Baseer	Mulla Habibullah	Tokhai Nozai	Pishin	Dilsora	96	Village Tokhai Nozai, UC Dilsora, Tehsil Karezat, District Pishin	Allah Noor	54303-7366001-9
32	Murad Khan	Gul Meer	Shaqa Samalzai	Pishin	Dilsora	37	Village Shaqa Samalzai, UC Dilsora, Tehsil Karezat, District Pishin	Allah Noor	54301-2382602-9

GOAT DISTRIBUTION LIST (FARMERS)

S. No.	Name of Farmer	Husband/Father's Name	Tag No	Name of WCO	Name of SM	NIC No
MASTUNG						
1	Lal Bibi	Abdul Aziz	26	Moqadus	Hajra Shah	51602-1089753-4
2	Alam Bibi	Mola dad	13	Bushamzai	Samina Zafar	51602-3238877-4
3	Khurshida	Ibrahim Khan	29	Sawalkhanzai	Hajra Shah	516023507451-5
4	Bibi	Bhengo Khan	10	Syed Zai	Hajra Shah	51602-1094308-8
5	Sakina	Hazoor Bakhsh	38	Ash Khan (Gulab)	Hajra Shah	51602-0490701-6
6	Amna	Nazar Muhammad	4	Ash Khan (Chumbali)	Hajra Shah	51602-1145867-3
7	Zer Bibi	Manji (Juma Khan)	16	Ash Khan (Gulab)	Hajra Shah	51602-0490701-6
8	Shah Peri	Ghulam Qadir	56	Jarr Zai	Samina Zafar	51602-5220163-0
9	Gunj bibi	Musa Khan	18	Sammarzai	Samina Zafar	51602-664007-7
KHUZDAR						
1	Somari	Mohammad Hassan	79	Alangi	Sahira Baloch	51401-7172964-8
2	Lal Bibi	Ali Mohammad	31	Alangi	Sahira Baloch	51401-5667285-1
3	Khair bibi	Khair Bakhsh	51	Peepali	Sahira Baloch	627-15-031786
4	Hajira	Mohammad	80	Peepali	Sahira Baloch	51401-8982306-2
5	Ruqia	Mohammad Ramzan	55	Peepali	Sahira Baloch	51401-3725550-2
6	Maryam	Sulaiman	92	Bunap	Nasima Khalil	627-89-327652
7	Haneefa	Dilmuraed	77	Bunap	Nasima Khalil	627-50-139036
8	Amina	Bakhshal	74	Ali Hasan	Nasima Khalil	627-40-040813
9	Sameena	Ali Hasan	78	Ali Hasan	Nasima Khalil	627-86-634258
10	Naz Bibi	Abdull Qadir	33	Marrav	Nasima Khalil	51401-903252-0
KALAT						
1	Zulekha	Muhammad Alam	30	Muhammad Zai	Kiran	51202-4964673-1
2	Hanifa	Lal Bakhsh	8	Roshan Abad	Kiran	626-41-150614
3	Zarina	Dur Mohd	76	Chad Trasani	Shaista	51202-2068515-0
4	Jamal khatoon	Atta ullah	81	Chad Trasani	Shaista	51202-1737924-0
5	Janat khatoon	Hassan bux	12	Mengal Abad 1	Shaista	626-56-041533
6	Noor khatoon	Shakar khan	82	Mengal Abad 1	Shaista	627-88-376926
7	Zubeda	Mohd sharif	2	Mengal Abad 2	Kiran	627-59-147300
8	Maryam	Muhammad Amin	14	Mengal Abad 2	Kiran	626-57-055049
9	Fatima	Muhammad Saeed	11	Roshan Abad	Kiran	626-83-246936
10	Hajira	Muhammad Ishaq	5	Shori	Kiran	626-53-152709
ZIARAT						
1	Mosima	Juma Khan	27	Killi Ghabergai	Sameen Jamali	55402-4632226-5
2	Bibi Afghana	Rasooldad	53	Kill Lal Muhammad	Sameen Jamali	55402-1563189-7
3	Niaz Bibi	Amir Muhammad	71	Killi Marghloon	Sameen Jamali	55402-2156047-2
4	Bibi Satira	Late Sarghar	32	Killi Sherin Pitawo	Sameen Jamali	55402-9023747-0
5	Noor Bai	Allah Jan	48	Killi Salo Landi	Sameen Jamali	609-93-315820
6	Salima Bibi	Abdullah Shah	50	Killi Hassanabad	Sameen Jamali	55402-4727165-1
7	Akhter Bibi	Samand Khan	90	Poi Ada	Sameen Jamali	55402-2972432-3
8	Momina	Khudaidad	65	New Poi Ada Hospital	Sameen Jamali	609-92-0466-87
9	Zahida	Fateh Shah	61	New Poi Ada Hospital	Sameen Jamali	55402-1562688-5
QUETTA						
1	Naik Bibi	Naik Muhammad	2	Ghaibzai Almar	Amina Shah	54400-7573982-1
2	Bibi Noor	Malik Fazal	22	Ghaibzai Almar	Amina Shah	54400-0916009-9
3	Zarina	Haji Rasheed	83	Ghaibzai Almar	Amina Shah	54400-7573982-1
4	Farida	Abdul Khaliq	84	Bangul Abdulzai	Amina Shah	54400-6742985-9
5	Bibi Naz	Muhammad Rafiq	63	Khoni Talab	Ayesha Shah	54400-0412236-7
6	Yasmeen	Muhammad Akram	93	Khoni Talab	Ayesha Shah	54400-9116151-5
7	Bakht Bibi	Saleh Muhammad	44	Killi Abdul Raheem	Ayesha Shah	54400-4922474-1
8	Shah Tareen	Bahauddin	70	Killi Abdul Raheem	Ayesha Shah	54400-3082460-5
9	Maira Bibi	Akhter Muhammad	52	Killi Abdul Raheem	Ayesha Shah	54400-0411723-7

GOAT DISTRIBUTION LIST (FARMERS)

S. No.	Name of Farmer	Husband/Father's Name	Tag No	Name of WCO	Name of SM	NIC No
PISHIN						
1	Qafia	Dadullah	9	Mazvai	Amina Khan	54302-25679508
2	Bibi Maryam	Payo Khan	11	Bala Jhalak	Amina Khan	54302-59304385-5
3	Bakhtawara	Jamal Shah	8	Kuz Woobashkai	Amina Khan	54302-86749170-8
4	Sadia	Muhammad Iqbal	14	Kuz Woobashkai	Amina Khan	54302-1483274-8
5	Shafia	Muhammad Ameer	15	Jane Alaka	Amina Khan	602-51-214569
6	Muhammadzai	Abdul Majeed	12	Tokhai Nozai	Amina Khan	54302-07563304
7	Bibi Hawa	Mohibullah	16	Wolong Ghara	Amina Khan	54302-8757895-4
8	Bibi Alima	Salih Muhammad	17	Sogai Dargai	Amina Khan	54301-08865828
9	Nasira	Abdul Hameed	1	Wolong Ghara	Amina Khan	54302-0787119-7
LORALAI						
1	Babai	Baik Khan	5	Sara Kalla	Rubina	609-94-099190
2	Sabira	Juma Khan	25	Sara Kalla	Rubina	609-27-09882
3	Bakhai	Hashim	44	Nali Mulazai	Rubina	609-88-271840
4	Sahibo	Baran	97	Nali Mulazai	Rubina	609-48-170821
5	Naik Bakhta	Sofi	92	Dolat China	Rubina	609-44-117250
6	Balai	Waray	63	Gidawal Bala	Raheela	56302-9389766-2
7	Kaghai	Soleman	38	Gul Kach	Raheela	609-93-179656
8	Azadi	Musa	54	Aqrabi	Raheela	56302-9916651-1
9	Gul Khanda	Malak	6	Sarwazd	Raheela	609-33-024062
10	Baddo	Kharh	71	Gul Kach	Raheela	56302-0824991-9
QILA SAIFULLAH						
1	Saleha	Khuda i Dad	18	Idrees Talarai	Naz Gul	56202-5518798-06
2	Palwasha	Aminullah	29	Idrees Talarai	Naz Gul	56202-01033185-01
3	Shah Peri	Abdul Hakeem	39	Zaghaloon	Naz Gul	56202-0951376-5
4	Shahida	Habibullah	53	Asozai	Naz Gul	56202-0983825-7
5	Fairoza	Muhammad Gul	20	Asozai	Naz Gul	56202-0906543-2
6	Ameera	Ameer Muhammad	19	Asozai	Naz Gul	612-51-058397
7	Meena	Faqir Muhammad	23	Raheemgul Kareez	Naz Gul	56202-0963780-7
8	Sahiba	Abdul Ghafoor	31	Killi Sangar	Fouzia Saif	54302-4762589-3
9	Jan Bibi	Zainullah	21	Killi Sangar	Fouzia Saif	56202-4457449-2

List of Chicks Birds Distribution 2007

S. No	Name of Woman Farmer	Husband/Father's Name	No of Birds (Female 10+2 Male)	Name of WCO	Name of SM	CNIC No
MASTUNG						
1	Salaha	Ghulam uddin	12	Gulab zai(Moqadus)	Hajra Shah	51602-0272644-6
2	Safia	Rasool Bakhsh	12	Gulab zai(Moqadus)	Hajra Shah	51602-3448237-3
3	Zer jan	Abdul Hameed	12	Sawal khan Zai (Karan)	Hajra Shah	51602-0689038-0
4	Zanab	Muhammad Jan	12	Sawal khan Zai (Karan)	Hajra Shah	51602-1125079-7
5	Tahira	Abdullah Shah	12	Sawal Khan Zai (Karan)	Hajra Shah	51602-2827808-4
6	Ayeshah	Behram Khan	12	Notak zai	Hajra Shah	51602-5968180-2
7	Fatama	Zaman	12	Notak zai	Hajra Shah	51602-7896339-3
8	Noor Bakht	Noor Muhammad	12	Notak zai	Hajra Shah	616-52-096634
9	Fatama	M. Murad	12	Syed Zai	Hajra Shah	54400-3311711-8
10	Bibi dur	Abdullah Shah	12	Syed Zai	Hajra Shah	51602-6751948-4
11	Meher jan	Abdullah Shah	12	Syed zai	Hajra Shah	51692-6751948-4
12	Jmal Khatoon	Ghulam Farooq	12	Ash khan (gulab)	Hajra Shah	51602-1090573-0
13	Noor Bibi	Lal Muhammad	12	Ash khan (Chambili)	Hajra Shah	51602-5675717-2
14	Noor Bakht	Qadir Bakhsh	12	Ash khan	Hajra Shah	51602-1145807-1
15	Lal bibi	Pir Bakhsh	12	Ash khan	Hajra Shah	51602-1984050-2
16	Khair bib	Gul M. Din	12	Ash khan (bishamzai	Samina Zafar	51602-2445715-2
17	Zakara	Wali Muhammad	12	Basham Zai (Gulab)	Samina Zafar	51602-1098322-8
18	Amna	Muhammad Azam	12	Basham Zai	Samina Zafar	5102-3230349-6
19	Lal Khatoon	Sher Muhammad	12	Basham Zai	Samina Zafar	51602-7162868-0
20	Gul khatoon	Rustum Khan	12	Jarr Zai	Samina Zafar	6045173606
21	Abida	Hazoor Bakhsh	12	Jarr zai	Samina Zafar	51602-1092029-2
22	Tahira	Noor Bakhsh	12	Jarr zai	Samina Zafar	51602-581536-9
23	Khan bibi	Noor Muhammad	12	Sammar zai	Samina Zafar	626-20-140951
24	Khailo	Muhammad Rahim	12	Sammar zai	Samina Zafar	51602-402541-4
25	Lal bibi	Muhammad jan	12	Jar zai _2	Samina Zafar	51602-402541-4
26	Hajra	Qadir Bakhsh	12	Ash Khan (Gulab)	Hajra Shah	54102-1549340-5
ZIARAT						
1	Bakhtvai	Abdul Haleem	12	Killi Amanullah Aghbergai	Sameen Jamali	55402-2078622-1
2	Naik Bibi	Abdul Kareem	12	Killi Lal Muhammad	Sameen Jamali	55402-1852155-9
3	Bibi Safar Jana	Abdullah Jan	12	Killi Sherin Pitawo	Sameen Jamali	55402-5377801-4
4	Bibi Zahira	Noor Muhammad	12	Killi Sherin Pitawo	Sameen Jamali	55402-1009157-8
5	Gul Bibi	Mehmood Khan	12	Killi Sherin Pitawo	Sameen Jamali	55402-9023747-0
6	Tabai (batai)	Kamal Khan	12	Killi Sherin Pitawo	Sameen Jamali	609-35-165278
7	Alai	Lal Muhammad	12	Killi Salo Landi	Sameen Jamali	55402-6105090-4
8	Jahan Bakht	Noor Muhammad	12	Killi Salo Landi	Sameen Jamali	55402-7518560-4
9	Narangai	Fateh Shah	12	Killi Salo Landi	Sameen Jamali	609-46-046686
10	Balgisa	Abdul Ghafoor	12	Killi Salo Landi	Sameen Jamali	55402-4206057-1
11	Fatima Bibi	Umer	12	Killi Hassanabad	Sameen Jamali	55402-0669747-9
12	Sabira Bibi	Abdul Samad	12	Killi Hassanabad	Sameen Jamali	609-86-247666
13	Hidaya Bibi	Ahmed Noor	12	Killi Hassanabad	Sameen Jamali	55402-2730022-1
14	Bakhtnama Bibi	Kuhday Raheem	12	Killi Hassanabad	Sameen Jamali	55402-1564136-1
15	Saira Bibi	Juma Khan	12	Killi Hassanabad	Sameen Jamali	55402-1565854-9
16	Amina Bibi	Roza Khan	12	Poi Ada	Sameen Jamali	609-60-317260
17	Guldasta	Abdullah Khan	12	Poi Ada	Sameen Jamali	55402-5998115-5
18	Asia Khan	Samand Khan	12	Poi Ada	Sameen Jamali	55402-1567099-1
19	Bibi Rozmina	Aminullah	12	Poi Ada	Sameen Jamali	609-88-012683
20	Raz Bibi	Mulla Juma	12	Poi Ada	Sameen Jamali	55402-1567099-1
21	Koter	Muhammad Shah	12	New Poi Ada Hospital	Sameen Jamali	55402-1566941-7
22	Mastoor	Ghulam Ishaq	12	New Poi Ada Hospital	Sameen Jamali	55402-0669747-9
23	Rakia	Abdullah	12	New Poi Ada Hospital	Sameen Jamali	609-52160210
24	Lal Gulla	Abdul Qudoos	12	New Poi Ada Hospital	Sameen Jamali	55402-1562669-7
25	Bulbula	Ahmed Shah	12	New Poi Ada Hospital	Sameen Jamali	55402-1566821-7
26	Siraj bibi	Akhter Muhammad	12	Killi Shaizai	Sameen Jamali	55402-1567969-5
27	Noor Bibi	Bakhtair	12	Killi Shah Khuza	Sameen Jamali	55402-6493738-1
28	BB Koter	Zardad Khan	12	Killi Ghabargi	Sameen Jamali	55402-21564462-5

List of Chicks Birds Distribution 2007

S. No	Name of Woman Farmer	Husband/Father's Name	No of Birds (Female 10+2 Male)	Name of WCO	Name of SM	CNIC No
QUETTA						
1	Fatima	Abdul Haq	12	Ghaibzai Almar	Amina Shah	54400-0373443-6
2	Raqima	Saifullah	12	Ghaibzai Almar	Amina Shah	54400-0412123-6
3	Zarghona	Alam Khan	12	Ghaibzai Almar	Amina Shah	54400-4069821-1
4	Bibi Zaiba	Abdul Ghani	12	Ghaibzai Almar	Amina Shah	54400-0402270-6
5	Bkakhtawar	Wali Muhammad	12	Ghaibzai Almar	Amina Shah	54400-0411162-7
6	Halima	Haji Azam	12	Bangle (Satara)	Amina Shah	54400-0416005-7
7	Zulakha	Lowang	12	Bangle (Satara)	Amina Shah	54400-0416005-7
8	Zar Khatoon	Konar Khan	12	Abdul Nabi	Amina Shah	54400-037187-2
9	Shahida	Muhammad Younis	12	Bangle (Satara)	Amina Shah	54400-3145683-3
10	Zulakha	Haji Muhammad Gul	12	Killi Serwer	Amina Shah	54400-0544563-9
11	Tahira	Nazar Muhammad	12	Killi Serwer	Amina Shah	54400-0407066-6
12	Palwasha	Abdul Shakoor	12	Killi Serwer	Amina Shah	54400-0399443-1
13	Raqima	Ghafar	12	Killi Serwer	Amina Shah	54400-0460782-1
14	Khair Zadi	Wahid Bakhsh	12	Abdul Nabi	Amina Shah	54400-834717-3
15	Rahima	Abdul Hakeem	12	Abdul Nabi	Amina Shah	54400-0401488-5
16	Jam Zadi	Khuda Bakhsh	12	Abdul Nabi	Amina Shah	54400-0401488-3
17	Noor Khatoon	Shareef Ahmed	12	Abdul Nabi	Amina Shah	54400-0516506-3
18	Shaheen	Allah Bakhsh	12	Abdul Nabi	Amina Shah	51602-1139860-9
19	Sakina	Rahem Dil	12	Abdul Nabi	Amina Shah	54400-0401488-3
20	Jam Bibi	Khair Din	12	Abdul Nabi	Amina Shah	54400-0401255-7
21	Rasheeda	Rasool Bakhsh	12	Khooni Talab	Ayesha Shah	54400-0412233-9
22	Fareeda	Attaullah	12	Khooni Talab	Ayesha Shah	54400-0412230-1
23	Raj Bibi	Kamal Khan	12	Ghaibzai	Ayesha Shah	54400-0411735-1
24	Bibi Nafeesa	Muhammad Yousaf	12	Killi Sinjdi	Ayesha Shah	54400-0378075-6
25	Sabra	Abdul Manan	12	Killi Sinjdi	Ayesha Shah	54400-0410966-9
26	Zargul	Muhammad Ibrahim	12	Killi Sinjdi	Ayesha Shah	54400-0411034-9
27	Jannat Khatoon	Rehmatullah	12	Killi Sinjdi	Ayesha Shah	54400-1489600-9
28	Bibi Zohra	Muhammad Naeem	12	Killi Abdul Raheem	Ayesha Shah	54400-0411699-7
PISHIN						
1	Fatima	Muhammad Yousaf	12	Koz Obeshkai	Amina Khan	54302-84286343-0
2	Akhtarzai	Muhammad Younis	12	Koz Obeshkai	Amina Khan	54302-0760741-4
3	Sabira	Amir Jan	12	Koz Obeshkai	Amina Khan	54302-2181069-6
4	Sakhula	Zahir Shah	12	Koz Obeshkai	Amina Khan	54302-7379169-8
5	Yasmeen	Ghulam Muhammad	12	Bala Jhalak	Amina Khan	54302-0540763-1
6	Bakhtawara	Abdul Majeed	12	Bala Jhalak	Amina Khan	54302-6777589-8
7	Noor Bibi	Ali Muhammad	12	Bala Jhalak	Amina Khan	54301-09104307
8	Podina	Abdul Samad	12	Bala Jhalak	Amina Khan	54302-69694439
9	Gul Khanda	Muhammad Hashim	12	Jane Alka	Amina Khan	54301-55306015
10	Bibi Husmina	Khan Muhammad	12	Jane Alka	Amina Khan	54301-1657672-8
11	Alia	Abdul Malik	12	Jane Alka	Amina Khan	54301-091741-1
12	Hajira	Shamsullah	12	Jane Alka	Amina Khan	604-93-205288
13	Shafia	Sultan Muhammad	12	Muzvai	Amina Khan	54302-0778281-7
14	Shafia	Nooruddin	12	Muzvai	Amina Khan	54301-5638653-8
15	Zulekha	Umai	12	Muzvai	Amina Khan	54301-0915894-3
16	Halima	Abdul Samad	12	Muzvai	Amina Khan	54301-0913827-1
17	Shah Bibi	Abdul Qayum	12	Tokhai Nozai	Amina Khan	54301-0916099-7
18	Bibi Alisa	Rozi Deen	12	Tokhai Nozai	Amina Khan	54303-7366009-1
19	Bibi Maryam	Boor Muhammad	12	Tokhai Nozai	Amina Khan	54301-0911044-5
20	Bibi Sahub Jana	Muhammad Ayub	12	Tokhai Nozai	Amina Khan	54301-7037642-4
21	Bibi Fateema	Abdul Sattar	12	Wolong Ghara	Amina Khan	54302-0761555-4
22	Zar Gula	Abdul Jabbar	12	Wolong Ghara	Amina Khan	54302-0761581-4
23	Bibi Noor Jahan	Abdul Karim	12	Wolong Ghara	Amina Khan	54302-0758169-2
24	Bibi Ayesha	Agha Muhammad	12	Wolong Ghara	Amina Khan	604-75-203228
25	Shafia	Nooruddin	12	Sogai Dargai	Amina Khan	54301-5638653-8
26	Fateema	Bismillah	12	Sogai Dargai	Amina Khan	54301-0891155-8
27	Shafia	Said muhammad	12	Sogai Dargai	Amina Khan	604-43-008284

List of Chicks Birds Distribution 2007

S. No	Name of Woman Farmer	Husband/Father's Name	No of Birds (Female 10+2 Male)	Name of WCO	Name of SM	CNIC No
LORALAI						
1	Baulata	Rozi Khan	12	Sara Kalla	Robina	609-58-023437
2	Naik Bakhta	Sada Gul	12	Sara Kalla	Robina	56302-0847602-5
3	Majahra (Sabira)	Zareen	12	Sara Kalla	Robina	609-46-098344
4	Wobash	Lahore	12	Sara Kalla	Robina	609-51-096579
5	Bainazeer	Abdul Rahim	12	Sara Kalla	Robina	609-55-098440
6	Qayamata	Zareen	12	Dolat China	Robina	56302-0850788-3
7	Zargula	Meera Jan	12	Dolat China	Robina	609-58-028528
8	Mandeena	Yaqoob	12	Dolat China	Robina	609-39-117249
9	Saido	Qalander Khan	12	Dolat China	Robina	56302-8911677-1
10	Noor Nama	Safar Khan	12	Dolat China	Robina	56302-4424157-5
11	Gul Naseeb Bibi	Chiragh	12	Gidawal Bala	Raheela	56302-1660196-5
12	Wanna	Payo	12	Gidawal Bala	Raheela	56302-8201038-5
13	Panjabi	Sher Muhammad	12	Gidawal Bala	Raheela	56302-1660196-5
14	Garano	Mastak	12	Gidawal Bala	Raheela	609-56-098434
15	Gul Peri	Muhammad khan	12	Gidawal Bala	Raheela	56302-5446309-3
16	Tajo (Momina)	Fazal Karim	12	Sarwazd	Raheela	56302-0837850-3
17	Zar Bano (Ailana)	Santullah	12	Sarwazd	Raheela	56302-9841000-0
18	Doulata (Bakht Bibi)	Wahab	12	Sarwazd	Raheela	56302-0837811-5
19	Kunai (Gul Bakhta)	Bahar	12	Sarwazd	Raheela	56302-1405534-1
20	Bakhtnoora (Shareen)	Akhtar Zaman	12	Sarwazd	Raheela	56302-5653584-9
21	Gul Bakhat	Ramazan	12	Aqrabi	Raheela	56302-0825003-5
22	Bakhtilai	Shinwari	12	Aqrabi	Raheela	609-88-028383
23	Sabira	Landai	12	Aqrabi	Raheela	609-55-098842
24	Tatai	Jalal Khan	12	Aqrabi	Raheela	609-47-116192
25	Gul Nama	Sada Gul	12	Aqrabi	Raheela	609-57-239918
26	Karko	Muhammad Din	12	Nali Mulazai	Robina	609-57-028767
27	Shareeno	Jan uddin	12	Nali Mulazai	Robina	56302-2415024
QILA SAIFULLAH						
1	Shah Peri	Abdul Hakeem	12	Zaghaloon	Naz Gul	56202-0951376-5
2	Fatima	Sarwar	12	Zaghaloon	Naz Gul	56202-3107977-4
3	Podeena	Usman	12	Zaghaloon	Naz Gul	56202-08877618-03
4	Asia	Allah Noor	12	Killi Asozai	Naz Gul	56202-6473350-9
5	Noor Bibi	Asad Khan	12	Killi Asozai	Naz Gul	56202-3961897-0
6	Khalida	Kaleemullah	12	Killi Asozai	Naz Gul	56202-639648-6
7	Fairoza	Muhammad Gul	12	Killi Asozai	Naz Gul	56202-0906543-2
8	Ameera	Ameer Muhammad	12	Killi Asozai	Naz Gul	612-51-058397
9	Rukhsana	Hedayatullah	12	Killi Asozai	Naz Gul	56202-0963820-9
10	Shahida	Habibullah	12	Killi Asozai	Naz Gul	56202-0983825-7
11	Abida	Muhammad Hashim	12	Killi Asozai	Naz Gul	612-51-058397
12	Rabia	Qalandar Khan	12	Makhai Kareez	Naz Gul	56202-924407-6
13	Fateema	Amanullah	12	Makhai Kareez	Naz Gul	602-51-155678
14	Zalaja	Shahabuddin	12	Makhai Kareez	Naz Gul	56202-090565-0
15	Qasima	Muhammad Essa	12	Makhai Kareez	Naz Gul	56202-0907567-04
16	Sherina	Gul Khan	12	Makhai Kareez	Naz Gul	56202-6740807-6
17	Gul Seema	Zaitullah	12	Makhai Kareez	Naz Gul	56202-0887073-0
18	Khalida	Muhammad Sarwer	12	Zaghaloon	Naz Gul	56202-3107977-4
19	Noorzia	Muhammad Azam	12	Zaghaloon	Naz Gul	56202-6810476-5
20	Qasima	Ameer Muhammad	12	Zaghaloon	Naz Gul	56202-0905603-4
21	Zahida	Peer Muhammad	12	Takai Kareez	Naz Gul	56202-9907666-7
22	Darana	Shahabuddin	12	Takai Kareez	Naz Gul	56202-7976660-7
23	Zakeera	Muhammad Murad	12	Takai Kareez	Naz Gul	56202-561592-8
24	Haleesa	Agha Muhammad	12	Takai Kareez	Naz Gul	602-38-186343
25	Taj Bibi	Niaz Muhammad	12	Takai Kareez	Naz Gul	56202-8213836
26	Laina	Gul Muhammad	12	Takai Kareez	Naz Gul	56202-346854-6
27	Amina		12	Rahimgul Kareez	Naz Gul	

List of Chicks Birds Distribution 2007

S. No	Name of Woman Farmer	Husband/Father's Name	No of Birds (Female 10+2 Male)	Name of WCO	Name of SM	CNIC No
KALAT						
1	Zakia	Muhammad Rafiq	12	Muhammad Zai	Kiran	626-49-007097
2	Gul pari	Raz Muhammad	12	Muhammad Zai	Kiran	51202-5580006-1
3	Noor khatoon	Kareem Jan	12	Muhammad Zai	Kiran	51202-4221931-7
4	Hoor bibi	Abdul Razaq	12	Muhammad Zai	Kiran	51202-1631859-8
5	Rehmat khatoon	Goram Khan	12	Muhammad Zai	Kiran	627-90-331494
6	Faiz bibi	Abdul Qadir	12	Roshan Abad	Kiran	51202-8736789-3
7	Bilqees	Muhammad Ashraf	12	Roshan Abad	Kiran	51703-0339522-9
8	Busnaz (Bianaz)	Ali bux	12	Roshan Abad	Kiran	626-48-041557
9	Sakina	Gulam Hassan	12	Roshan Abad	Kiran	51202-8708370-3
10	Naz bibi	Abdul Razaq	12	Roshan Abad	Kiran	51202-4961402-7
11	Merjan	Murad Bakhsh	12	Shaikh Hussain	Kiran	51202-6672269-4
12	Shazadi	Razzaque	12	Shaikh Hussain	Kiran	51202-5294867-0
13	Noor bibi	Hafiz Abdul khaliq	12	Shaikh Hussain	Kiran	51202-1579371-7
14	Bus Khatoon	Haji	12	Shaikh Hussain	Kiran	51202-788677-3
15	Grahnaz	Ismail	12	Shaikh Hussain	Kiran	51202-8344398-3
16	Zaib un nisha	Muhammad Yousaf	12	Chad Trasani	Shaista	607-43-151447
17	Bibi Hawa	Raz Muhammad	12	Chad Trasani	Shaista	51202-1275907-2
18	Noor khatoon	Sona	12	Chad Trasani	Shaista	626-93-217023
19	Khair un Nisa	Muhammad Sharif	12	Chad Trasani	Shaista	626-46-055990
20	Farida	Abdul Satar	12	Mengal Abad 1	Shaista	51202-5319462-9
21	khatija	Saleh Muhammad	12	Mengal Abad 1	Shaista	626-90-107348
22	Zulekha	Muhammad Rahim	12	Mengal Abad 1	Shaista	626-93-219698
23	Lal bibi	Niaz Muhammad	12	Mengal Abad 1	Shaista	51202-8137869-3
24	Qimati	Qadir Bux	12	Mengal Abad 2	Kiran	626-48-147174
25	Amina	Muhammad Amin	12	Mengal Abad 2	Kiran	626-53-036411
26	Noor Jan	Nazir Ahmed	12	Mengal Abad 2	Kiran	51202-8137869-3
27	Bas Khatoon	Shadi khan	12	Mengal Abad 2	Kiran	51202-1073735-2
KHUZDAR						
1	Shah bibi	Mohammad Noor	12	Alangi	Sahira Baloch	627-8-12821
2	Khair bibi	Mohammad Alam	12	Alangi	Sahira Baloch	51401-0671968-5
3	Khadija	Mohammad	12	Alangi	Sahira Baloch	51401-2238800-7
4	Hajira	Mohammad Ashraf	12	Alangi	Sahira Baloch	627-64-22190
5	Rahima	Abdul Qadir	12	Peepali	Sahira Baloch	51401-8266187-8
6	Madina bibi	Allah Bakhsh	12	Peepali	Sahira Baloch	51401-1106170-8
7	Khan bibi	Krim Bakhsh	12	Peepali	Sahira Baloch	627-50-031784
8	Noor bibi	Mohammad Hayat	12	Jauri	Sahira Baloch	51401-2286394-5
9	Kazbano	Abdul Haque	12	Jauri	Sahira Baloch	627-88-322786
10	Zainab	Lal Mohammad	12	Jauri	Sahira Baloch	627-52-086391
11	Zubaida	Imam Bakhsh	12	Jauri	Sahira Baloch	51401-2214642-2
12	Naz bibi	Attaullah	12	Jauri	Sahira Baloch	51401-2286394-1
13	Qaim Khatoon	Ghulam Mustafa	12	Jauri	Sahira Baloch	51401-2281453-5
14	Zubaida	Abdullah	12	Bunap	Nasima Khalil	51401-498598-5
15	Hidayath	Muhammad Ibrahim	12	Bunap	Nasima Khalil	627-36-204376
16	Maryam	Muhammad Ameen	12	Bunap	Nasima Khalil	627-53-138211
17	Sakeena	Abdul Khaliq	12	Bunap	Nasima Khalil	51401-498598-5
18	Fatima	Esmail	12	Ali Hasan	Nasima Khalil	627-43-081161
19	Haneefa	Mohammad Hayat	12	Ali Hasan	Nasima Khalil	627-92-245941
20	Murad Khatoon	Khan Mohammad	12	Ali Hasan	Nasima Khalil	627-58-252237
21	Maryam	Sumail	12	Ali Hasan	Nasima Khalil	627-97-341751
22	Yasmeen	Obadullah	12	Marrav	Nasima Khalil	51401-9469448-8
23	Farida	Fateh Mohammad	12	Marrav	Nasima Khalil	627-59-138773
24	Shams Khatoon	Bashir Ahmad	12	Marrav	Nasima Khalil	627-88-326736
25	Zenab	Mohammad Eshaq	12	Marrav	Nasima Khalil	51401-6110505-9
26	Taj Bibi	Abdul Nabi	12	Marrav	Nasima Khalil	51401-2280705-7
27	Zohra	Abdul Khaliq	12	Bunap	Nasima Khalil	
28	Raj Bibi	Dil murad	12	Bunap	Nasima Khalil	

List of PSI Schemes (Water Sector)

Schemes	S. No.	Name of MCO/WCO	Comm. Share	ADPB Share	Total Cost (PKR)	Beneficiaries
Lined Water Storage Reservoir, Channel & UPVC Pipe for Agriculture Purpose	1	Kuz Jhalak	115886	269701	385587	91
	2	Walang	73794	172185	245979	77
	3	Lower Jhalak	90082	210190	300272	105
	4	Sogi Dargi	84374	196872	281246	105
	5	Ghara Walang	118982	277626	396608	91
	6	Kuz Obeshkai	111733	260711	372444	140
	7	Killi Shasa Ismail Zai	149899	349765	499664	161
	8	Kuz Shakh	149277	348313	497590	91
	9	Muzvai	116625	272124	388749	175
	10	Tokhi Nozai	116625	272124	388749	91
	11	Abdulzai	82194	191787	273981	140
	12	Zaghloona	60241	140563	200804	112
	13	Ali Ghat	187809	438221	626030	112
	14	Idrees Talari	246698	575628	822326	112
	15	Lalo Zai	119765	279453	399218	105
	16	Marpal I	90508	211185	301693	105
	17	Marpal II	86120	200947	287067	105
	18	Dolat Cheena	197298	460363	657661	84
	19	Hasan Abad Poi	182541	425928	608469	119
	20	Shaizai	185321	432417	617738	91
	21	Shireen Pitao	185321	432417	617738	112
	22	Salo Landi	185321	432417	617738	91
Water Supply Schemes	23	Sogi Dargi	110213	257163	367376	105
	24	Jane Alak	62877	146714	209591	77
	25	Kuz Obeshkai	53139	123992	177131	140
	26	Ghabizai	93135	217316	310451	140
	27	Bungul	47612	111094	158706	105
	28	Makhi Karez	46400	108268	154668	112
	29	Shaizai	54736	127716	182452	91
	30	Marghaloon Chotair	85184	198763	283947	91
	31	Bataar	50952	118887	169839	105
	32	Jauri	52535	122583	175118	84
	33	Banap	65660	153207	218867	154
	34	Jo Parco	52535	122583	175118	147
	35	Roshan Abad I	54112	126264	180376	182
	36	Chud Trasani	75770	176797	252567	154
	37	Mengal Abad	60685	141599	202284	105
Karez Rehab.	38	Rahim Gul Karez	74925	174825	249750	126
	39	Makhi Karez	90450	211050	301500	112
	40	Lalozai	95512	222863	318375	105
	41	Jo Parco II	53325	124425	177750	105
Spring Rehab.	42	Dolat Cheena	20464	47748	68212	84
	43	Chuki Noghay	34650	80850	115500	105
High Efficiency Irr. System	44	Sargkalan	5400	129820	135220	7
	45	Amanzai Akrabia	32400	142782	175182	7
	46	Molvi Lal Muhammad	12600	133524	146124	7
	47	Graib Abad	13500	304724	318224	7
	48	Sanari	66960	202318	269278	7
Solar & Wind Based Energy System	49		0	1104000	1104000	840
			4402145	11982812	16384957	5719

**Cutting & Sewing Training & Details of Beneficiaries of Sewing Machines
Supported by World Food Programme
Status as of December 31, 2007**

District	Training Dates	Valley Name	Beneficiary Name	Father/ husband's Name	NIC	NIC Owner	Designation	CO Name	Poverty Profile	Trainer	Responsible
Training in Khuzdar - Parko valley											
1 Khuzdar	22-Aug	8-Sep Parko	Amina	Lal Mohammed	627-50-139261	Husband	Manager	Jo Parko I	farmer	Razia	Naseema
2 Khuzdar	22-Aug	8-Sep Parko	Rehmat Khatoon	Mohammed Iqbal	627-92-099789	Husband	Member	Jo Parko I	Landless	Razia	Naseema
3 Khuzdar	22-Aug	8-Sep Parko	Hasina	Nisar Mohammed	51401-2214690-8	Father	Member	Jo Parko I	Widow	Razia	Naseema
4 Khuzdar	22-Aug	8-Sep Parko	Sahib Khatoon	Naseer Ahmed	51401-4414962	Self	President	Jo Parko I	farmer	Razia	Naseema
5 Khuzdar	22-Aug	8-Sep Parko	Khadija	Mohammed Baksh	51401-2223530-8	Husband	Member	Jo Parko I	tenant	Razia	Naseema
6 Khuzdar	22-Aug	8-Sep Parko	Raj Bibi	Mohammed Haris	627-53-025092	Self	Member	Jo Parko I	Wage labour	Razia	Naseema
7 Khuzdar	22-Aug	8-Sep Parko	Hasina Begum	Mir Mohammed Noor	627-93-007659	Father	Member	Jo Parko I	Widow	Razia	Naseema
8 Khuzdar	22-Aug	8-Sep Parko	Farzana	Ghulam Sarwar	51401-4837410-9	Self	Member	Jo Parko I	Wage labour	Razia	Naseema
9 Khuzdar	22-Aug	8-Sep Parko	Amina	Haji Ghulam Rasul	627-76-344633	Father	Member	Batar	Unemployed	Razia	Naseema
10 Khuzdar	22-Aug	8-Sep Parko	Ruqya	Mohammed Ramzan	51401-7937049	Husband	Member	Batar	Unemployed	Razia	Naseema
11 Khuzdar	22-Aug	8-Sep Parko	Zenab	Mohammed Rahim	51401-0161462-3	Husband	Member	Batar	Wage labour	Razia	Naseema
12 Khuzdar	22-Aug	8-Sep Parko	Zarina	Mohammed Hayat	51401-8496256-5	Father	Member	Batar	Unemployed	Razia	Naseema
13 Khuzdar	22-Aug	8-Sep Parko	Bibi Amina	Mohammed Hayat	51404-02852325-0	Father	Member	Batar	Unemployed	Razia	Naseema
14 Khuzdar	22-Aug	8-Sep Parko	Maryam	Ghulam Nabi	51401-2453283-0	Self	Manager	Batar	Landless	Razia	Naseema
15 Khuzdar	22-Aug	8-Sep Parko	Amina	Mohammed Ali	627-46-055992	Husband	Member	Batar	Wage labour	Razia	Naseema
Training in Kalat - Gidder valley											
16 Kalat	19-Sep	4-Oct Gidder I	Hajira	Mohammed Ishaq	626-53-152709	Self	Manager	Shori		Perveen	Kiren
17 Kalat	19-Sep	4-Oct Gidder I	Rabia	Abdul Hakeem	626-57-126956	Brother	Member	Shori	Wage labour	Perveen	Kiren
18 Kalat	19-Sep	4-Oct Gidder I	Lal Bibi	Juma Khan	626-45-031235	Self	Member	Shori	Widow	Perveen	Kiren
19 Kalat	19-Sep	4-Oct Gidder I	Murad Bibi	Mohammed Khan	626-30-011037	Self	Member	Shori	Wage labour	Perveen	Kiren
20 Kalat	19-Sep	4-Oct Gidder I	Noor Bibi	Peer Jan	626-26-063772	Self	Member	Shori	landless	Perveen	Kiren
21 Kalat	19-Sep	4-Oct Gidder I	Hidayat Khatoon	Ghulam Haider	626-57-129977	Self	Member	Shori	Unemployed	Perveen	Kiren
22 Kalat	19-Sep	4-Oct Gidder I	Hajira	Mohammed Ibrahim	626-93-217258	Self	Not CO member	Shori	Wage labour	Perveen	Kiren
23 Kalat	19-Sep	4-Oct Gidder I	Noor Khatoon	Mohammed	421-75-358949	Self	Member	Shori Mengal	Wage labour	Perveen	Kiren
24 Kalat	19-Sep	4-Oct Gidder I	Fatima	Mohammed Ramzan	51202-6766602-4	Mother-in-law	Member	Shori Mengal	Unemployed	Perveen	Kiren
25 Kalat	19-Sep	4-Oct Gidder I	Rabia	Mohammed Anwer	51202-8938939-9	Self	Member	Shori Mengal	Unemployed	Perveen	Kiren
26 Kalat	19-Sep	4-Oct Gidder I	Abdia	Mohammed	626-93-217679	Brother-in-law	Manager	Shori Mengal	Wage labour	Perveen	Kiren
27 Kalat	19-Sep	4-Oct Gidder I	Safia	Attaullah	626-84-245760	Brother-in-law	Member	Shori Mengal	Wage labour	Perveen	Kiren
28 Kalat	19-Sep	4-Oct Gidder I	Sajida	Mohammed Ishaq	51202-9985774-5	Self	Member	Shori Mengal	Wage labour	Perveen	Kiren
29 Kalat	19-Sep	4-Oct Gidder I	Zahida	Abdul Kareem	626-93-057575	Father-in-law	Member	Shori Mengal	Wage labour	Perveen	Kiren
30 Kalat	19-Sep	4-Oct Gidder I	Bibi Ayesha	Haji Nazar Mohamed	51202-1790047-9	Father	Not CO member	Shori Mengal	Landless	Perveen	Kiren
Training in Qila Saifullah - Kan Mehtarzai valley											
31 Qila Saifullah	3-Oct	29-Oct Kan Mehtarzai	Sakeena	Mohibullah	56202-0963136-9	Husband	Member		Labour	Shamim	Nazgul
32 Qila Saifullah	3-Oct	29-Oct Kan Mehtarzai	Bibi Noor Jan	Kamal Khan	56202-0911496-0	Self	Member	New Lalozai	Labour	Shamim	Nazgul
33 Qila Saifullah	3-Oct	29-Oct Kan Mehtarzai	Bibi Razia	Sultan Mohammed	56202-2903121-0	Self	Member	New Lalozai	Unemployed	Shamim	Nazgul
34 Qila Saifullah	3-Oct	29-Oct Kan Mehtarzai	Amina	Paand Khan	56202-0956837-5	Father	Member	New Lalozai	Labour	Shamim	Nazgul
35 Qila Saifullah	3-Oct	29-Oct Kan Mehtarzai	Jameela	Kala Khan	56202-5276317-3	Father	Member	New Lalozai	Mine Labour	Shamim	Nazgul
36 Qila Saifullah	3-Oct	29-Oct Kan Mehtarzai	Sajida	Kamal Khan	56202-0952491-1	Father	Member	New Lalozai	Labour	Shamim	Nazgul
37 Qila Saifullah	3-Oct	29-Oct Kan Mehtarzai	Hameeda	Daulat Khan	56202-0956837-5	Husband	Member	Lalozai Karez	Landless	Shamim	Nazgul
38 Qila Saifullah	3-Oct	29-Oct Kan Mehtarzai	Amina	Rozuddin	56202-8411329-1	Husband	Member	Lalozai Karez	Very poor	Shamim	Nazgul

39	Qila Saifullah	3-Oct	29-Oct	Kan Mehtarzar	Hanifa	Sultan Mohammed	56202-4170814-4	Self	Member	Lalozai Karez	Unemployed	Shamim	Nazgul
40	Qila Saifullah	3-Oct	29-Oct	Kan Mehtarzar	Sursanda	Raz Gul	56202-7329324-7	Husband	Member	Lalozai Karez	Land tenant	Shamim	Nazgul
41	Qila Saifullah	3-Oct	29-Oct	Kan Mehtarzar	Sadiqa	Peer Mohammed	56202-9309732-5	Brother	Member	New Lalozai	Unemployed	Shamim	Nazgul
42	Qila Saifullah	3-Oct	29-Oct	Kan Mehtarzar	Zubaida	Abdul Hakim	56202-0951358-5	Father	Member	Lalozai Karez	Mine Labour	Shamim	Nazgul
43	Qila Saifullah	3-Oct	29-Oct	Kan Mehtarzar	Shapal	Abdul Hakim	56202-0951376-5	Father	Member	Lalozai Karez	Widow	Shamim	Nazgul
44	Qila Saifullah	3-Oct	29-Oct	Kan Mehtarzar	Bibi Hawa	Nil	Nil	NA	Member	Rahim Gul Karez	Labour	Shamim	Nazgul
45	Qila Saifullah	3-Oct	29-Oct	Kan Mehtarzar	Poodena	Nil	Nil	NA	Member	Lalozai Karez	Widow	Shamim	Nazgul
Training in Khuzdar - Tootak valley													
46	Khuzdar	22-Oct	10-Nov	Tootak	Shah Bibi	Manzoor Ahmed	627-88-326627	Self	Member	Chokynoghay I	Wage labour	Razia	Saira
47	Khuzdar	22-Oct	10-Nov	Tootak	Janat Khatoon	Abdul Hameed	51401-2215310-8	Self	Member's daughter	Chokynoghay I	Wage labour	Razia	Saira
48	Khuzdar	22-Oct	10-Nov	Tootak	Zarina	Ghulam Hussain	51401-1807023-6	Self	Member	Chokynoghay I	Unemployed	Razia	Saira
49	Khuzdar	22-Oct	10-Nov	Tootak	Parveen	Abdul Razzaq	51401-2278527-1	Husband	Member's daughter	Chokynoghay I	Unemployed	Razia	Saira
50	Khuzdar	22-Oct	10-Nov	Tootak	Rehmat Khatoon	Ghulam Faruq	51401-2223867-0	Self	Member	Chokynoghay I	Unemployed	Razia	Saira
51	Khuzdar	22-Oct	10-Nov	Tootak	Hasina	Amanullah	627-90-328856	Self	Member	Chokynoghay I	Unemployed	Razia	Saira
52	Khuzdar	22-Oct	10-Nov	Tootak	Shakar Khatoon	Abdul Rauf	51401-0365092-4	Self	Member	Chokynoghay I	Wage labour	Razia	Saira
53	Khuzdar	22-Oct	10-Nov	Tootak	Razia	Gul Hassan	51401-9792204-9	Father	Member's daughter	Chokynoghay I	Wage labour	Razia	Saira
54	Khuzdar	22-Oct	10-Nov	Tootak	Salim Khatoon	Niaz Ahmed	51401-1371318-0	Self	Member	Chokynoghay I	Wage labour	Razia	Saira
55	Khuzdar	22-Oct	10-Nov	Tootak	Bilqeesa	Jan Mohammed	627-80-385099	Self	Member	Chokynoghay I	Labour	Razia	Saira
56	Khuzdar	22-Oct	10-Nov	Tootak	Toba	Hassan Ali	51401-2295916-1	Father	Member's daughter	Chokynoghay II	Labour	Razia	Saira
57	Khuzdar	22-Oct	10-Nov	Tootak	Bilqeesa	Abdul Ghani	51401-8968462-1	Father	Member's daughter	Chokynoghay II	Labour	Razia	Saira
58	Khuzdar	22-Oct	10-Nov	Tootak	Rabia	Abdul Hayee	627-77-170044	Father	Member	Chokynoghay II	Labour	Razia	Saira
59	Khuzdar	22-Oct	10-Nov	Tootak	Rehana	Abdul Hakeem	51401-9633184-7	Father	Member	Chokynoghay II	Unemployed	Razia	Saira
60	Khuzdar	22-Oct	10-Nov	Tootak	Jan Gul	Mohammed Azeem	51401-1642282-1	Husband	Member	Chokynoghay II	Unemployed	Razia	Saira
61	Khuzdar	22-Oct	10-Nov	Tootak	Yasmeen	Qadir Ali	627-58-147336	Father	Member's daughter	Chokynoghay II	Unemployed	Razia	Saira
62	Khuzdar	22-Oct	10-Nov	Tootak	Khatija	Habibullah	627-63-245674	Father	Member's daughter	Chokynoghay II	Unemployed	Razia	Saira
63	Khuzdar	22-Oct	10-Nov	Tootak	Hajira	Mohammed Murad	627-22-195418	Husband	Member	Chokynoghay II	Unemployed	Razia	Saira
64	Khuzdar	22-Oct	10-Nov	Tootak	Zulekha	Abdul Qayyum	51401-7885817-3	Husband	Member	Chokynoghay II	Unemployed	Razia	Saira
65	Khuzdar	22-Oct	10-Nov	Tootak	Rehmat Khatoon	Jamsheer Khan	627-43-182396	Husband	Member	Chokynoghay II	Unemployed	Razia	Saira
Training in Kalat - Gidder valley													
66	Kalat	22-Oct	7-Nov	Gidder I	Hidayat Khatoon	Abdul Ghani	626-78-245792	Self	Member	Killi Sanari	Widow	Perveen	Kiren
67	Kalat	22-Oct	7-Nov	Gidder I	Zubaida	Sanaullah	626-72-027239	Brother-in-law	Member	Killi Sanari	labour	Perveen	Kiren
68	Kalat	22-Oct	7-Nov	Gidder I	Sabira	Abdul Samad	51202-6838099-0	Self	Member	Killi Sanari	labour	Perveen	Kiren
69	Kalat	22-Oct	7-Nov	Gidder I	Hanifa	Mohammed Kareem	51202-4911200-6	Self	Member	Killi Sanari	labour	Perveen	Kiren
70	Kalat	22-Oct	7-Nov	Gidder I	Lal Bibi	Kareem Baksh	51202-1787265-5	Father	Member	Killi Sanari	Unemployed	Perveen	Kiren
71	Kalat	22-Oct	7-Nov	Gidder I	Shahzadi	Ghulam Mustafa	51202-0516282-5	Self	Member	Killi Sanari	Unemployed	Perveen	Kiren
72	Kalat	22-Oct	7-Nov	Gidder I	Mah bibi	Ghulam Nabi	51202-6824283-3	Self	Member	Killi Sanari	Unemployed	Perveen	Kiren
73	Kalat	22-Oct	7-Nov	Gidder I	Sharbano	Hameedullah	626-83-247004	Self	Member	Killi Sanari	labour	Perveen	Kiren
74	Kalat	22-Oct	7-Nov	Gidder I	Hidayat Khatoon	Abdul Nabi	626-55-027237	Self	President	Killi Sanari	labour	Perveen	Kiren
75	Kalat	22-Oct	7-Nov	Gidder I	Fateh Khatoon	Abdul Kareem	51202-7742668-4	Self	Manager	Mal Lashkari	labour	Perveen	Kiren
76	Kalat	22-Oct	7-Nov	Gidder I	Shah Bibi	Noor Baksh	51202-9454721-1	Self	Member	Mal Lashkari	labour	Perveen	Kiren
77	Kalat	22-Oct	7-Nov	Gidder I	Haseena	Ahmed Ali	51202-1787184-1	Self	Member	Mal Lashkari	labour	Perveen	Kiren
78	Kalat	22-Oct	7-Nov	Gidder I	Farida	Mohammed Ali	51202-2722525-1	Self	Member	Mal Lashkari	labour	Perveen	Kiren
79	Kalat	22-Oct	7-Nov	Gidder I	Hameeda	Saifullah	51202-5746366-1	Self	Member	Mal Lashkari	labour	Perveen	Kiren
80	Kalat	22-Oct	7-Nov	Gidder I	Safia	Abdul Majeed	51202-4526949-1	Self	Member	Mal Lashkari	labour	Perveen	Kiren
81	Kalat	22-Oct	7-Nov	Gidder I	Naz Bibi	Asadullah	51202-6503648-2	Self	Member	Mal Lashkari	Unemployed	Perveen	Kiren
82	Kalat	22-Oct	7-Nov	Gidder I	Begum	Mohammed Ibrahim	626-85-025859	Self	Member	Mal Lashkari	Unemployed	Perveen	Kiren
83	Kalat	22-Oct	7-Nov	Gidder I	Ganj Bibi	Jamal Din	626-90-107234	Self	Member	Mal Lashkari	labour	Perveen	Kiren
84	Kalat	22-Oct	7-Nov	Gidder I	Shakar Bibi	Rasul Baksh	51202-1787185-3	Self	President	Mal Lashkari	labour	Perveen	Kiren
85	Kalat	22-Oct	7-Nov	Gidder I	Zulekha	Abdul Wahid	51202-1787186-3	Self	Manager	Mal Lashkari	shopkeeper	Perveen	Kiren

Training in Qilia Saifullah - Kan Mehtarzai valley												
	7-Nov	25-Nov	Amna	Allah Noor	56202-5331580-2	Self	Member	Sur Karez	Labour	Shamim	Fouzia Saif	
86	Qilia Saifullah	7-Nov	Kan Mehtarzai	Amna	Allah Noor	56202-5331580-2	Self	Member	Sur Karez	Shamim	Fouzia Saif	
87	Qilia Saifullah	7-Nov	Kan Mehtarzai	Sarsanda	Ahmed Jan	56202-4056210-2	Self	Member	Sur Karez	Shamim	Fouzia Saif	
88	Qilia Saifullah	7-Nov	Kan Mehtarzai	Amna	Noorullah	56202-532509-2	Self	Member	Sur Karez	Shamim	Fouzia Saif	
89	Qilia Saifullah	7-Nov	Kan Mehtarzai	Sadla	Muhammed Noor	56202-09556184-3	Husband	Member	Sur Karez	Shamim	Fouzia Saif	
90	Qilia Saifullah	7-Nov	Kan Mehtarzai	Fatima	Rozi Khan	56207-3953924-5	Son	Member	Sur Karez	Shamim	Fouzia Saif	
91	Qilia Saifullah	7-Nov	Kan Mehtarzai	Gul Sabza	Kaleem	56202-0910906-5	Husband	Member	Sangar I	Shamim	Fouzia Saif	
92	Qilia Saifullah	7-Nov	Kan Mehtarzai	Rasheeda	Salahuddin	56202-2291473-4	Self	Member	Sangar I	Shamim	Fouzia Saif	
93	Qilia Saifullah	7-Nov	Kan Mehtarzai	Ayesha	Abdul Wahab	56202-0964823-1	Father	Member	Sangar I	Shamim	Fouzia Saif	
94	Qilia Saifullah	7-Nov	Kan Mehtarzai	Jan Bibi	Zainullah	612-65-088132	Husband	Member	Sangar I	Shamim	Fouzia Saif	
95	Qilia Saifullah	7-Nov	Kan Mehtarzai	Haleema	Mohibullah	56202-9541045-3	Husband	Member	Sangar I	Shamim	Fouzia Saif	
96	Qilia Saifullah	7-Nov	Kan Mehtarzai	Rufia	Bak Mohammed	56202-8128083-8	Self	Member	Sangar I	Shamim	Fouzia Saif	
97	Qilia Saifullah	7-Nov	Kan Mehtarzai	Sahiba	Fakharuddin	54302-4762589-3	Husband	Member	Sangar I	Shamim	Fouzia Saif	
98	Qilia Saifullah	7-Nov	Kan Mehtarzai	Zarijuma	Noor Khan	56202-1620265-3	Husband	Member	Sangar II	Shamim	Fouzia Saif	
99	Qilia Saifullah	7-Nov	Kan Mehtarzai	Zalija	Shah Mohammed			Member	Sangar II	Shamim	Fouzia Saif	
100	Qilia Saifullah	7-Nov	Kan Mehtarzai	Farida (Paında)	Dost Mohammed	56202-0951708-3	father	Member's daughter	Sangar II	Shamim	Fouzia Saif	
101	Qilia Saifullah	7-Nov	Kan Mehtarzai	Feroza	Gul Mohammed	56202-4939276-9	Husband	Member	Sangar II	Shamim	Fouzia Saif	
102	Qilia Saifullah	7-Nov	Kan Mehtarzai	Fatima	Khudai Dost			Member	Sangar II	Shamim	Fouzia Saif	
103	Qilia Saifullah	7-Nov	Kan Mehtarzai	Shah Tarina	Agha Mohammed	612-48-059867	Husband	Member	Sangar II	Shamim	Fouzia Saif	
104	Qilia Saifullah	7-Nov	Kan Mehtarzai	Rafiza	Juma Khan			President	Sangar II	Shamim	Fouzia Saif	
105	Qilia Saifullah	7-Nov	Kan Mehtarzai	Sharifa	Akhtar Mohammed			Member	Sangar II	Shamim	Fouzia Saif	
Training in Qilia Saifullah - Kan Mehtarzai valley												
106	Qilia Saifullah	29-Nov	Suri Mehtarzai	Rashida	Usman Ghani	56202-9441250-2	Self	Member	Isozai	Shamim	Nazgul	
107	Qilia Saifullah	29-Nov	Suri Mehtarzai	Khalida	Mohammed Gul	56202-6396486-8	brother	Manager	Isozai	Shamim	Nazgul	
108	Qilia Saifullah	29-Nov	Suri Mehtarzai	Asia	Allah Noor	56202-6473350-9	Husband	Member	Isozai	Shamim	Nazgul	
109	Qilia Saifullah	29-Nov	Suri Mehtarzai	Shahida	Habibullah	602-63-429677	Self	President	Isozai	Shamim	Nazgul	
110	Qilia Saifullah	29-Nov	Suri Mehtarzai	Hassan Bibi	Nizamuddin	612-72-013725	Self	Member	Isozai	Shamim	Nazgul	
111	Qilia Saifullah	29-Nov	Suri Mehtarzai	Bibi Ayesha	Wali Mohammed	56202-0908503-0	Husband	Member	Rahim Gul Karez	Shamim	Nazgul	
112	Qilia Saifullah	29-Nov	Suri Mehtarzai	Bibi Sona	Abdul Kareem	56202-6227745-0	Husband	Member	Rahim Gul Karez	Shamim	Nazgul	
113	Qilia Saifullah	29-Nov	Suri Mehtarzai	Pari Gul	Fagir Mohammed	56202-7320822-6	Self	Member	Rahim Gul Karez	Shamim	Nazgul	
114	Qilia Saifullah	29-Nov	Suri Mehtarzai	Tahira	Atta Mohammed	56202-0960446-9	Husband	Member	Rahim Gul Karez	Shamim	Nazgul	
115	Qilia Saifullah	29-Nov	Suri Mehtarzai	Amina	Khuda Rahim	612-90-261382	Husband	Member	Rahim Gul Karez	Shamim	Nazgul	
116	Qilia Saifullah	29-Nov	Suri Mehtarzai	Sardar Bibi	Akhtar Mohammed	56202-797656-0	Husband	President	Takai Karez	Shamim	Nazgul	
117	Qilia Saifullah	29-Nov	Suri Mehtarzai	Khatima	Fazal Mohammed	56202-3468544-8	Husband	Member	Takai Karez	Shamim	Nazgul	
118	Qilia Saifullah	29-Nov	Suri Mehtarzai	Rabia	Ghazi Khan	612-21-057535	Husband	Member	Takai Karez	Shamim	Nazgul	
119	Qilia Saifullah	29-Nov	Suri Mehtarzai	Lubna	Gul Mohammed	56202-6396486-8	Self	Member	Takai Karez	Shamim	Nazgul	
120	Qilia Saifullah	29-Nov	Suri Mehtarzai	Robina	Jalauddin	612-88-057537	father	Manager	Takai Karez	Shamim	Nazgul	
Training in Khuzdar - Tootak valley												
121	Khuzdar	29-Nov	13-Dec	Parko	Sabira	noil	nil	member	Ali Hassan	Razia	Naseema	
122	Khuzdar	29-Nov	13 Dec	Parko	Karmia	noil	nil	Member	Ali Hassan	Razia	Naseema	
123	Khuzdar	29-Nov	13 Dec	Parko	Saleema	51401-2223867-0	father's	Manager	Ali Hassan	Razia	Naseema	
124	Khuzdar	29-Nov	13 Dec	Parko	Zainab	627-90-328756	Husband	Member	Ali Hassan	Razia	Naseema	
125	Khuzdar	29-Nov	13 Dec	Parko	Janat Khatoon	51401-0365092-4	father	Member	Ali Hassan	Razia	Naseema	
126	Khuzdar	29-Nov	13 Dec	Parko	Naz Bibi	51401-9792405-9	Husband	Member	Ali Hassan	Razia	Naseema	
127	Khuzdar	29-Nov	13 Dec	Parko	Hasina	51401-2067538-0	Husband	Member	Ali Hassan	Razia	Naseema	
128	Khuzdar	29-Nov	13 Dec	Parko	Fatima	51401-9792405-9	self	Member	Ali Hassan	Razia	Naseema	
129	Khuzdar	29-Nov	13 Dec	Parko	Bibi Naz	51401-9792405-9	father	Member	Ali Hassan	Razia	Naseema	

Annex 5

130	Khuzdar	29-Nov	13 Dec	Parko	Husna	Bashir Ahmed	51401-0960446-2	brother	Member	Ali Hassan	widow	Razia	Naseema
131	Khuzdar	29-Nov	13 Dec	Parko	Sakina	Ali Akbar	51401-9792405-9	self	Member	Marav	Unemployed	Razia	Naseema
132	Khuzdar	29-Nov	13 Dec	Parko	Murad Khatoon	Khan Mohammed	51401-3867567-9	Husband	Member	Marav	Unemployed	Razia	Naseema
133	Khuzdar	29-Nov	13 Dec	Parko	Hanifa	Mohammed Hayat	51401-3465790-4	Husband	Manager	Marav	tenant	Razia	Naseema
134	Khuzdar	29-Nov	13 Dec	Parko	Hasina	Mohammed Panah	627-92-234347	Father	Member's daughter	Marav	landowner	Razia	Naseema
135	Khuzdar	29-Nov	13 Dec	Parko	Zainab	Abdul Hamid	51401-5432967-8	self	Member	Marav	labour	Razia	Naseema
136	Khuzdar	29-Nov	13 Dec	Parko	Jumaiti	Abdul Qadir	51401-8320184-8	self	Member	Marav	labour	Razia	Naseema
137	Khuzdar	29-Nov	13 Dec	Parko	Zulekha	Bakshal	51401-3867567-9	self	Member	Marav	wage labour	Razia	Naseema
138	Khuzdar	29-Nov	13 Dec	Parko	Samina	Mohammed Baksh	51401-4136570-4	Self	Member	Marav	labour	Razia	Naseema
139	Khuzdar	29-Nov	13 Dec	Parko	Khairun nisa	Gulam Qadir	Nil	nil	Member	Ali Hassan	labour	Razia	Naseema
140	Khuzdar	29-Nov	13 Dec	Parko	Basra	Abdul Karim	627-87-283667	self	Member	Ali Hassan	TBA	Razia	Naseema

AREA DEVELOPMENT PROGRAMME BALOCHISTAN

ADPB/UNDP, 28-A Chaman Housing Scheme,
Airport Road, Quetta. G.P.O. Box # 107
Tel: +92-81-2864075 Fax: +92-81-2864076
Web: www.adpb.org.pk
