



ZANZIBAR PLANNING COMMISSION

CAPACITY BUILDING FOR SDGs AND MKUZA III COORDINATION AND REPORTING IN ZANZIBAR

Quarterly Project Progress Report (Quarter 2: April – June 2020)

Project Title: Capacity Building for SDGs and MKUZA III Coordination and Reporting

Country: United Republic of Tanzania

Reference: Agreement signed between ZPC and UNDP

Project Start Date: 01st September 2018

Project End Date: 30th June 2021

1. INTRODUCTION

The Revolutionary Government of Zanzibar is committed to the implementation of the Global Development Agenda 2030 as reflected in its development programs including the Zanzibar Strategy for Growth and Reduction of Poverty (MKUZA III). The Zanzibar Planning Commission is being supported by UNDP in implementing a project on ‘Capacity Building for SDGs and MKUZA III Coordination and Reporting in Zanzibar’.

The project is aimed at enhancing institutional capacities as well as putting in place an enabling policy and regulatory environment to facilitate coordination, monitoring and reporting of SDGs and MKUZA III. In addition to the ZPC, which is the Implementing Partner (IP), other key institutions involved in the implementation of this project include Office of the Chief Government Statistician (OCGS), Association of Non-Governmental Organizations in Zanzibar (ANGOZA) and the President Office, Communication Department.

This report is designed to present a detailed narrative of the activities and interventions implemented during April –June, 2020, in furtherance of the goal and objectives, of the project on ‘Capacity Building for SDGs and MKUZA III Coordination and Reporting in Zanzibar’. During the period under review, the focus was mainly on:

- i. Effective coordination and strategic leadership on SDGs and MKUZA III data for sustainable development established.
- ii. Improved national statistical frameworks and systems and
- iii. Strengthened multi-stakeholder partnerships for sustainable development data.

The following specific activities were implemented, and targets achieved during the quarter under review:

2. SIGNIFICANT ACHIEVEMENTS ON AGREED PLANNED ACTIVITIES AND OUTPUTS.

OUTPUT 1: Effective Coordination and Strategic Leadership on SDGS and MKUZA III Data for Sustainable Development established.

1.1. Develop M&E System and Tools

This activity involves engaging consultant to design, install and populate an electronic and operational M&E system with web-based database for National and International Strategies at the Zanzibar Planning Commission. During the quarter under review procurement process for engaging the consultant was initiated by ZPC Tender Board, and assignment is expected to commence during the 3rd quarter. The following deliverables are expected:

- An inception report that would provide a detailed description of the proposed methodology as well as the work plan;
- Draft designed and populated electronic and operational M&E system for ZPC and stakeholders;
- A final web-based socio-economic database (depository) for ZSGRP, SDGs and Agenda 2063 at the Zanzibar Planning Commission;
- Training package for ZPC staff including IT, data manager, M&E staff and stakeholders (MDAs, LGAs, and NSAs on how to use and manage an electronic M&E system and Web-based database at ZPC).
- The System Manual including the source codes.

This electronic database will enable ZPC and stakeholders to input, store and deposit data; facilitate different stakeholders to work under a wider area network; be capable to analyze data and generate tables, graphs and maps, as well as to outlay specific strategies, including: Agenda 2030, Agenda 2063, Zanzibar Development Vision and Medium Term Development Strategies.

1.2. Finalize Development of National Strategy for Development of Statistics (NSDS)

A draft National Strategy for the Development of Statistics (NSDS) which incorporates all needs from the sector plans is in place. The draft strategy has been reviewed by an international consultant and submitted for further finalization by the coordination team in collaboration with the local consultant. The final version is expected by the end of September 2020.

Output 2: Improved National Statistical Frameworks and Systems

2.1. Finalize the National Statistics Policy

This activity involved further refinement of the draft National Statistics Policy based on the comments provided by various stakeholders and further consultations with stakeholders of statistics from Unguja, Pemba and Mainland Tanzania. Various community and international groups including Government officials, decision makers, policy makers, academia, researchers, private sectors, civil society organizations, politicians, UN agencies through UNDP and others were consulted independently and their views have been well articulated at each stage of drafting this policy. It is currently under the relevant government policy making and approval process. The final version is expected by the end of September 2020.

Output 3: Strengthened Multi-stakeholder Partnerships for Sustainable Development Data.

3.1. Awareness creation on COVID 19 to Public in Zanzibar.

The objective of implementing this activity was to create awareness to civil society and local community on prevention and response to Corona Virus Disease (COVID 19). The implemented planned activities included:

- establishment of a technical team, involving representatives from the Ministry of Health, Zanzibar Planning Commission and two members from ANGOZA. The roadmap was

developed for the implementation of the activity and approved stickers and other messages before dissemination to the public.

- development of brochures and TV programs using Public TV of Zanzibar Broadcasting Corporation (ZBC), in consultation with officials from Ministry of Health



Technical team conduct the first meeting to develop road map for public awareness on prevention and response to COVID 19 awareness creation

- Establishment of CSOs online platform, whereby ANGOZA renewed its website including a web page specific for CORONA issues. Specific pages from social media were also launched in order to give people knowledge and information about Corona in Zanzibar. These pages from Facebook, Twitter and Instagram were given the same name #TUISHINDE CORONA ZANZIBAR. About 100 people visited the website per day and different comments like and share from the social media pages.



The specific page about Corona from Facebook

- Popularize preventive information: Brochures, Stickers and Posters were developed were developed to create awareness and understanding of the civil society on COVID 19

pandemic. They were disseminated to the public through social media while hard copies were distributed by ANGOZA staff in collaboration with a representative of NGO for Drivers and conductors. Hard copies of brochures were also distributed in the markets and shops. The brochures inform on COVID 19 symptoms and how to prevent people from getting COVID 19 disease. The stickers targeting passengers of public transport passengers were distributed in various routes in Unguja, as shown in below photo.



Staff distributing stickers in “Daladala” of Kisauni route to inform passengers on COVID 19

Posters were also printed and disseminated with the view of sensitizing the public on appropriate measures of washing hands in accordance to World Health Organization (WHO) directive.



ANGOZA staff sticking posters on a bucket of water for customers to wash their hands before receiving services

- Conducted TV and Radio programs: ANGOZA conducted a TV program on 10th of May 2020 through Zanzibar Broadcasting Corporation media, the program was live thus public got chance to ask question and clarification on what has been presented. The program was presented by the Executive Director of ANGOZA Mr Hassan Khamis Juma to inform the public on what Civil Society Organizations are doing in fighting against the

pandemic of Covid-19 where public in general was able to give their views and ask various questions for clarification.



The Interviewer from ZBC, Abubakar Harith with ANGOZA ,Executive Director , Mr Hassan Khamis and Awesu Ramadhan from JECA in a LIVE TV program

TUISHINDE CORONA ZANZIBAR

Kwa msaada zaidi Piga namba: 190 Huduma hii ni bure kwa mitandao yote

[f tuishindec corona](#)
[t tuishindec corona](#)
[i tuishindec corona](#)
[v Angoza tv](#)
[www.angoza.or.tz](#)
[info@angoza.or.tz](#)

KWA UFADHILI WA :-

TUME YA MIPANCO ZANZIBAR

Utangulizi

Homa kali ya mapafu inayosababishwa na Virusi vya Corona ni ugonjwa unaoambukizwa kwa kuingiwa na majimaji yatokayo kwenye njia ya hewa wakati mtu mwenye ugonjwa huu anapokohoa au kupiga chafya.

Njia nyingine ya maambukizi ni kwa kugusa majimaji yanayotoka puani (kamasi), kugusa vitambaa au nguo zilizotumiwa na mtu mwenye maambukizi ya ugonjwa huu, au maeneo mengine yaliyoguswa na mtu mwenye Virusi vya ugonjwa huu.

DALILI ZA HOMA YA CORONA

Homa

Kikohozi

Kubanwa mbavu na kupumua kwa shida

Vidonda kooni

Kuumwa kichwa

Mwili Kuchoka

Jinsi ya kujikinga na homa ya Virusi vya Corona

- Kaa umbali wa angalau zaidi ya mita 1 kati yako na mtu mwingine
- Funika mdomo na pua wakati wa kukohoa au kupiga chafya kwa kutumia kitambaa safi au sehemu ya mbele ya kiwiko cha mkono
- Epuka kusalimiana kwa kushikana mikono, kukumbatiana au kubusiana
- Epuka kujigusa macho, pua au mdomo
- Epuka matembezi au safari zisizo za lazima
- Epuka misongamano
- Safisha mikono yako mara kwa mara kwa maji tiririka na sabuni au tumia vitakasa mikono (sanitizer)
- Ukiona dalili za ugonjwa huu, wahi kituo cha huduma za afya
- Vile vile toa tarifa kwenye kituo cha huduma za afya uonapo mtu mwenye dalili za ugonjwa huu au piga simu namba: 190

Huduma hii ni bure kwa mitandao yote

Matibabu

Ugonjwa huu hauna chanjo wala tiba ya moja kwa moja, hivyo kama yalivyo magonjwa mengine yanayosababishwa na virusi, matibabu hufanyika kwa kuzingatia dalili zilizopo na ufuatiliaji wa karibu.

- Creating SMS and Phone Messages: ANGOZA has created messages of COVID 19 sent to its member's phone and community in general. The messages focused on 3 main areas. Firstly, how people to prevent themselves from COVID 19, Secondly Parents should keep

Success Story on COVID 19


Mr Maulid M Khamis is a Chairperson of an NGO called UMUZA (Umoja

their Children's at home and concentrate on their studies, Thirdly People should be doing exercise during their quarantine time. These messages were also sent over different peoples through regular

4. PROJECT MANAGEMENT SUPPORT

- 4.1 Support for project management during the period under review included training of implementing partners (IPs) and responsible parties (RPs) on communication and report writing in Dar es Salaam. This activity involved a total of 15 participants (6Female; 9Male). The training equipped the participants with cutting edge report writing skills which enable them to apply the acquired skills. During the training facilitator used different methodologies, including: Questions and Answers, Case studies, Group discussion and presentation, and power point presentations. The training covered many topics among them were:
- 4.2 Regarding achievements, the participants of workshop training gained knowledge on definition, types report and how to write good report. They also gained skills on presentation to audience and how to select appropriate style for presentation. It was advised that after the training the knowledge obtained had to be shared with the colleagues on both good report writing as well as presentation skills.

Graduation Ceremony on 5/06/2020

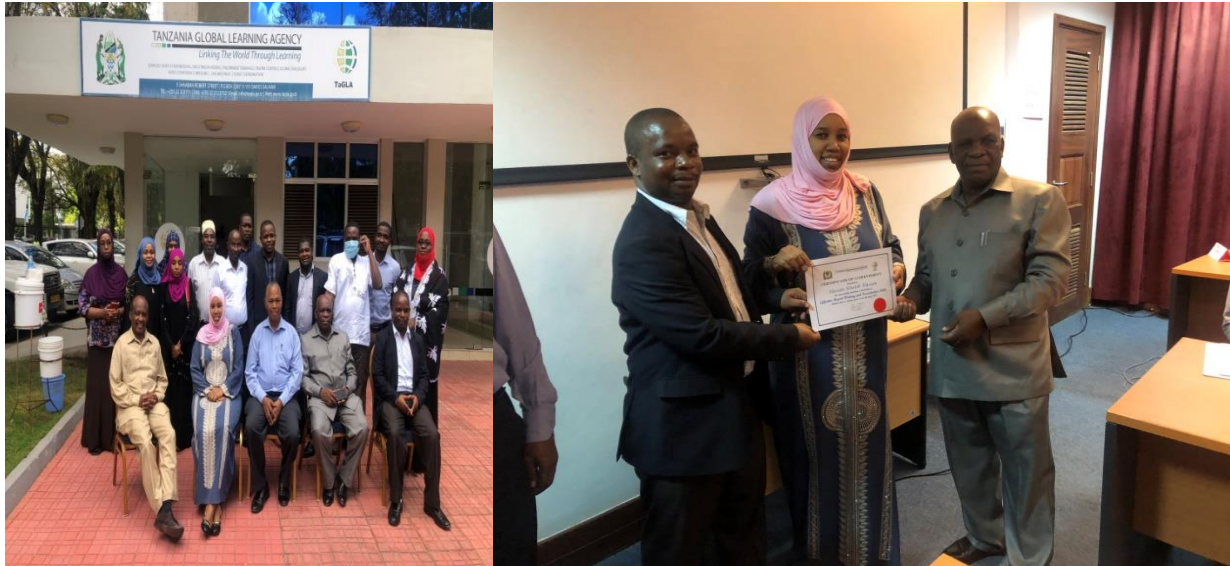

5. CHALLENGES

Delay in the disbursement of funds was experienced due to the reprogramming of UNDP projects aimed at responding to the COVID 19 pandemic. The delay affected timely implementation of most of the planned activities.

6. DISBURSEMENT

Given the limited utilization of the advance disbursed during the first quarter (21%). However, there were no resources disbursed during the quarter under review.

7. RESULTS MATRIX

Outcome 1: Strengthened Institutional Capacities in the Implementation, Monitoring and Reporting of SDGs and MKUZA III in Zanzibar			
Output	Planned Activity for Q1 (Implemented in Q2)	Status	Comments
Output 1: Effective coordination and strategic leadership on SDGs and MKUZA III data for sustainable development established	Develop M&E System and Tools	in progress	Procurement of the consultant was initiated.

Engagement with donor partners			
Output 2: Improved national statistical frameworks and systems	Finalize Development of National Strategy for Development of Statistics (NSDS)	in progress	The draft National Strategy for Development of Statistics (NSDS) developed
	Finalize the National Statistics Policy	in progress	The draft the National Statistics Policy in place
Output 3: Strengthened multi-stakeholder partnerships for sustainable development data.	Awareness creation on COVID 19 to Public in Zanzibar	Completed	<ul style="list-style-type: none"> • Preventive information such as stickers, Posters and brochures developed and distributed to the public • A TV program was aired on 10th of May 2020 through Zanzibar Broadcasting Corporation
Project Management Support	Training of Implementing Partner (IP) and Responsible parties (RPs) on communication and report writing	Completed	15 participants (6Female; 9Male) fully participated in the training and awarded certificates of completion
